


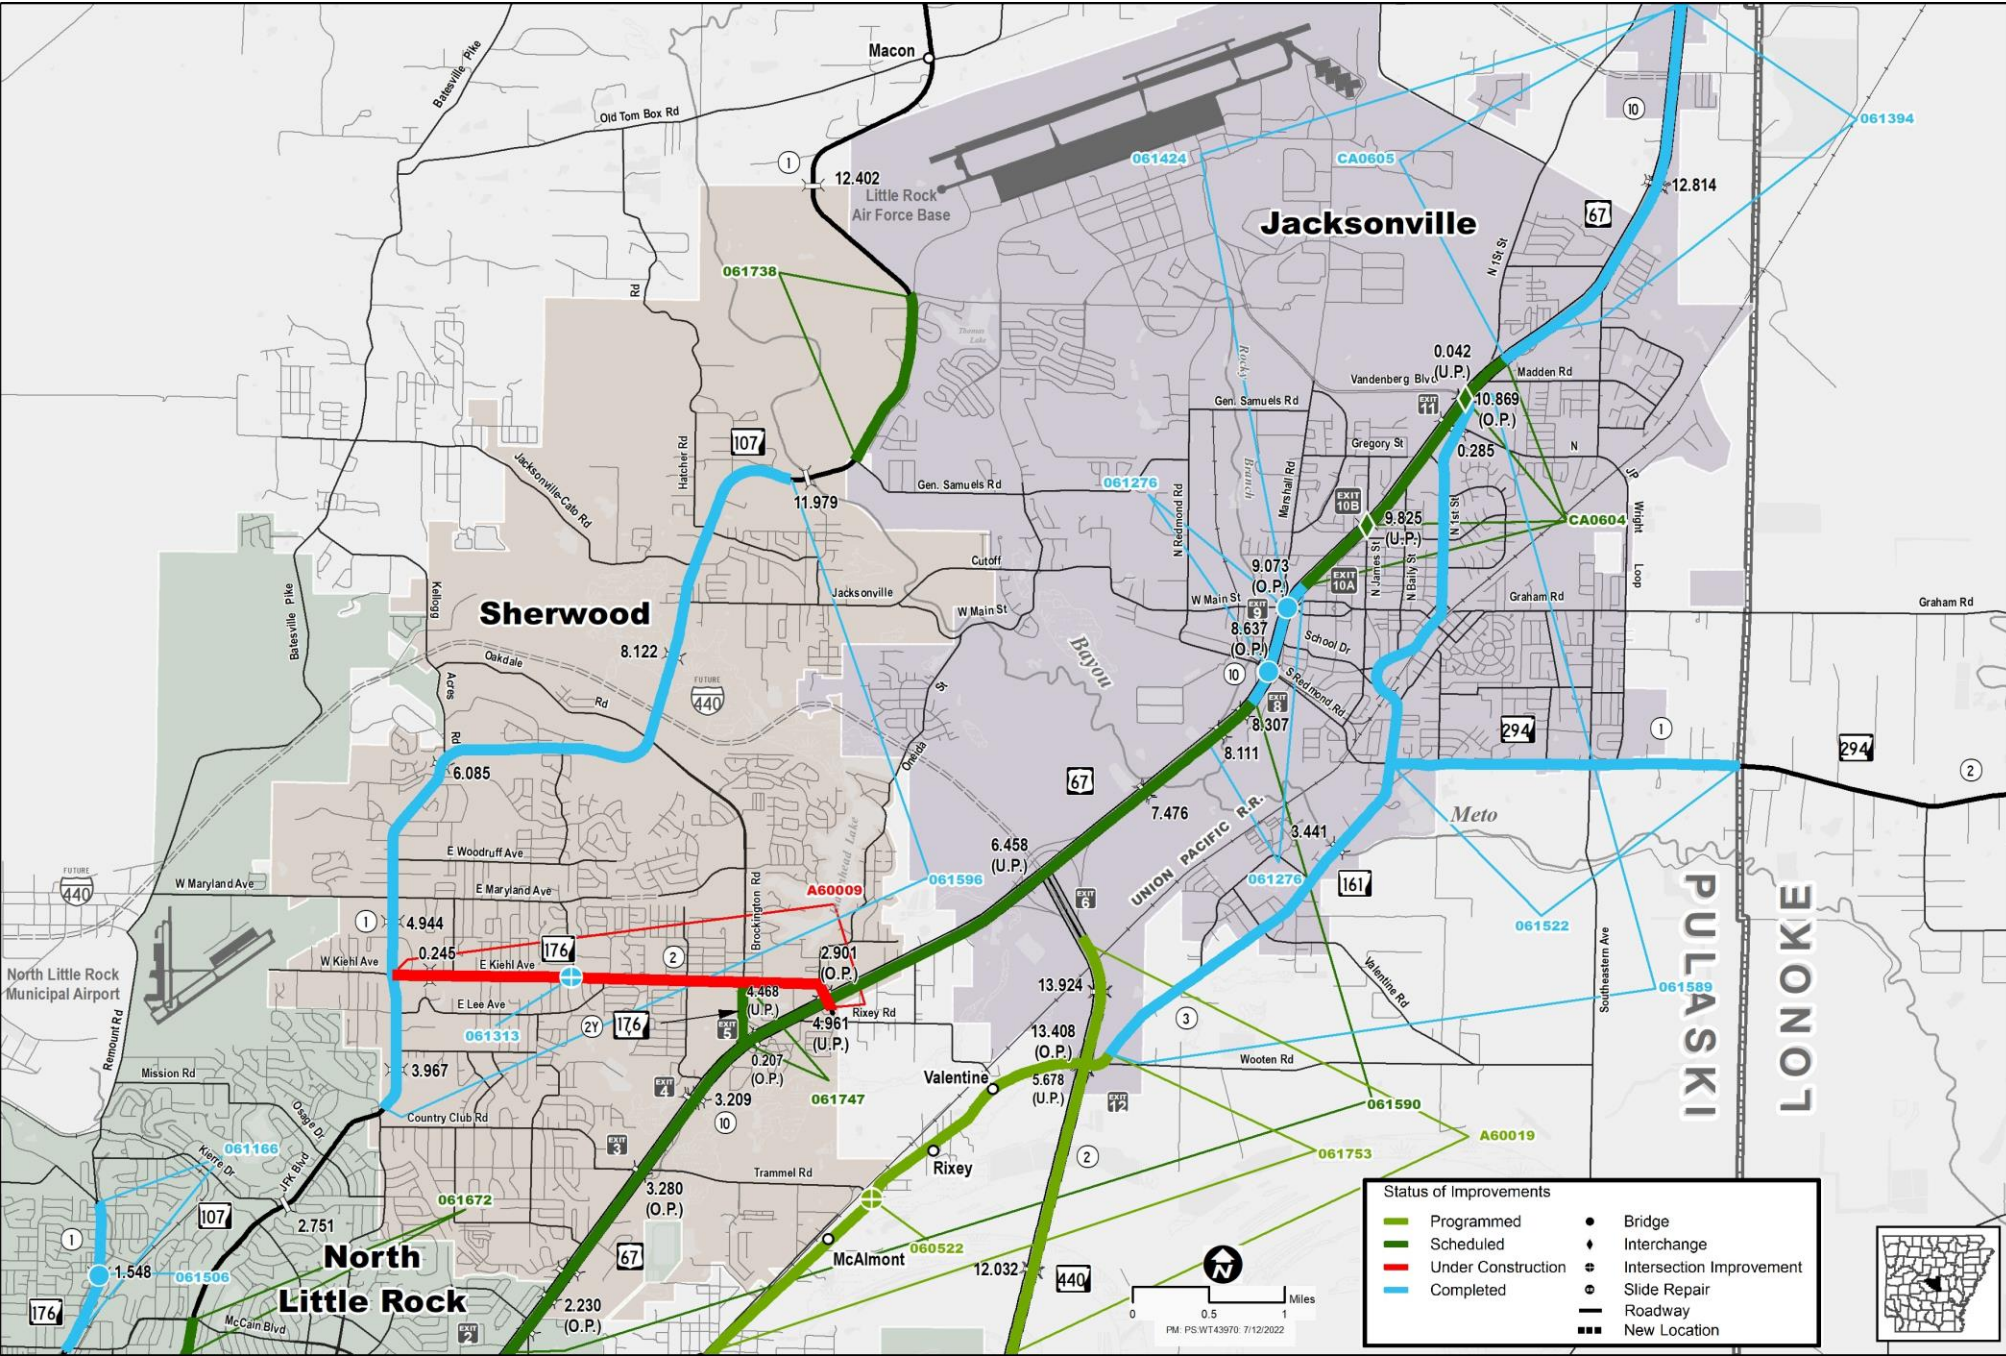

SUMMARY OF CONSTRUCTION PROJECTS

PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
001725*	Oklahoma Line – North Terminal P.E. Addt'l Rte.-Sec.: Various	40	33	PE Only	Completed		Aug. 2021	-	\$0	-	\$2,296,302
001727*	Texas Line – I-40 P.E. Addt'l Rte.-Sec.: Various	30	23	PE Only	Completed		Aug. 2021	-	\$0	-	\$3,541,398
012030*	I-30 & Hwy. 367 Navigation Lighting (L.R. & Newport) (S) Addt'l Rte.-Sec.: Jackson 367-21	30	23	Miscellaneous	Programmed			-	< \$1 M	-	< \$1 M
012119*	Conway – I-430 (Widening) P.E. Addt'l Rte.-Sec.: Faulkner 40-32	40	33	PE Only	Programmed			-	< \$1 M	-	< \$1 M
012145	Palarm Creek – Hwy. 365 (Widening) (F) Addt'l Rte.-Sec.: Faulkner 40-32	40	33	Major Widening	Completed	Sep. 2013	Dec. 2014	4.02	\$16,549,978	5.08	\$21,493,478
012177	No. Little Rock – St. Francis Co. Ln. (Sel. Secs.) (Cable Median Barrier) (S) Addt'l Rte.-Sec.: Lonoke 40-41; Monroe 40-43; Prairie 40-42	40	33	Safety Improvements	Completed	Feb. 2013	Sep. 2013	7.01	\$1,033,017	41.58	\$6,076,570
012296	Districts 2, 6, 7 & 8 Pavement Friction Impvts. (Sel. Secs.) (S) Addt'l Rte.-Sec.: Various	10	7	Safety Improvements	Completed	Jan. 2018	Oct. 2018	0.45	\$196,898	6.10	\$2,648,885
012343*	Overhead Sign Strs. & Signs Replacement (2020) (S) Addt'l Rte.-Sec.: Crittenden 55-11; Pulaski 430-21, 630-21, 67-10	30	23	Safety Improvements	Sub. Completed	Jun. 2020	Feb. 2022	-	\$2,628,738	-	\$2,891,612
012350*	Districts 2, 3, 6 & 7 Bridge Preservation (2020) (S) Addt'l Rte.-Sec.: Various	5	9	Bridge Rehabilitation	Completed	Apr. 2020	Mar. 2021	0.22	\$352,352	1.81	\$2,898,898
012357	Arkansas River Pier Protection Repairs (S) Addt'l Rte.-Sec.: Conway 9-7; Franklin 23-6	30	23	Emergency	Completed	May. 2020	Jan. 2021	0.58	\$800,214	1.23	\$1,697,005
012361*	Statewide UTBWC Impvts. (2020) (S) Addt'l Rte.-Sec.: Various			Safety Improvements	Under Construction	Nov. 2020	Late 2022	11.26	\$3,253,359	31.98	\$9,240,000
012362	Conway – North Little Rock (S) Addt'l Rte.-Sec.: Faulkner 40-32	40	33	Resurfacing	Scheduled	Nov. 2022		9.67	\$5 - \$10 M	22.66	\$15 - \$20 M
012387*	Statewide Underwater Br. Inspection (Phase XIII) (S) Addt'l Rte.-Sec.: Various	30	23	Miscellaneous	Programmed			-	-	-	-
012406*	Districts 1, 5, 6 & 10 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various			Bridge Rehabilitation	Under Construction	May. 2022	Mid 2023	-	\$2,421,021	-	\$7,187,312
012410*	Central AR – West Memphis ITS Impvts. Ph. 1 (S) Addt'l Rte.-Sec.: Various	30	23	Miscellaneous	Scheduled	Jun. 2023		-	\$3 - \$5 M	-	\$5 - \$10 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
012425*	Districts 2 & 6 Centerline Rumble Stripe Impvts. (S)			Safety Improvements	Under Construction	Apr. 2022	Early 2023	18.35	\$121,805	443.88	\$2,946,406
012440*	Central AR – West Memphis ITS Impvts. Ph. 2 (S)	70	13	Miscellaneous	Programmed			-	< \$1 M	-	\$5 - \$10 M
	Addt'l Rte.-Sec.: Various										
060352	McHenry Creek & Relief Strs. & Apprs. (S)	5	9	Structure & Approaches	Completed	Feb. 2012	Apr. 2013	0.31	\$2,499,527	0.31	\$2,499,527
060395	Union Pacific RR Overpass (Arch St.) (LR) (S)	367	13	Structure & Approaches	Completed	Dec. 2015	Nov. 2017	0.46	\$10,228,748	0.46	\$10,228,748
060450	Hwy. 338 Widening (E. of I-530) (S)	338	2	Major Widening	Programmed			0.36	\$1 - \$3 M	0.36	\$1 - \$3 M
060486*	I-630 Walkway Illumination (S)	630	0	Miscellaneous	Programmed			-	< \$1 M	-	< \$1 M
060522	Hwy. 161/Trammel Rd. Intersection Improvements (Sherwood) (S)	161	3	Safety Improvements	Programmed			-	< \$1 M	-	< \$1 M
060653*	I-430 – I-40 P.E.	100	0	PE Only	Programmed			-	-	-	-
060657*	I-30 – I-40 P.E.	430	21	PE Only	Completed		Aug. 2021	-	\$149,278	-	\$149,278
060658*	I-30 – I-40 (I-440)	440	1	PE Only	Programmed			-	-	-	-
060659*	I-430 – I-30 (I-630)	630	21	PE Only	Programmed			-	-	-	-
060696*	River Mtn. Rd. & Pleasant Valley Farm Rd. (LR) Surveys (S)	CS		PE Only	Programmed			-	-	-	-
060763*	District Six Overhead Sign Structures Replacement Repair (P.E.)			PE Only	Programmed			-	-	-	-
060907*	Geyer Springs R.R. Grade Separation (Little Rock) (S)	CS		RR Crossing	Under Construction	Aug. 2018		-	\$7,103,739	-	\$7,103,739
060949*	Little Rock & North Little Rock Wildflower Plantings (S)			Enhancement	Completed		Jun. 2022	-	\$26,795	-	\$26,795
061006*	Pulaski Co. Pedestrian/Bicycle Bridge (Murray Lock & Dam) (S)			Enhancement	Completed	Aug. 2004	Jun. 2016	-	\$10,609,687	-	\$10,609,687
061026*	Oak St. – Loop Rd. (Graham Rd.) (Jacksonville) (S)	CS		Major Widening	Completed	Oct. 2011	Jan. 2014	1.11	\$6,371,188	1.11	\$6,371,188
061080*	South Loop Bypass (Mabelvale Rd.-Alexander Rd.) (Little Rock) (S)	CS		Structure & Approaches	Completed	Feb. 2012	Sep. 2013	1.04	\$5,783,171	1.04	\$5,783,171
061094*	Baseline Rd. – J.E. Davis Dr. (Scott Hamilton Dr.) (L.R.) (S)	CS		Major Widening	Completed	Dec. 2013	Mar. 2015	0.54	\$2,248,581	0.54	\$2,248,581
061115*	I-630/Financial Center Pkwy./Shackleford Rd. Inters. Impvts. (S)	630	21	Study	Programmed			-	-	-	-
061119*	Rock Island Transp. Corridor Preservation (Pulaski Co.) (S)			Miscellaneous	Programmed			-	-	-	-
061121*	Little Rock Bike Connector P.E.	CS		Miscellaneous	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061148*	I-430/I-630 Interchange Modifications P.E.	430	21	PE Only	Completed		Jun. 2016	-	\$1,558,451	-	\$1,558,451
061161	I-430 East & West (Sel. Secs.) (Overlay) (S)	10	8	Resurfacing	Programmed			1.16	< \$1 M	1.16	< \$1 M
061166	47th St. – Remount Rd. Safety Impvts. (NLR) (S)	176	1	Safety Improvements	Completed	Jan. 2020	Jan. 2021	1.04	\$813,191	1.04	\$813,191
061190	I-40 Interchange (Maumelle) (S)	New		Interchange Improvements	Completed	Oct. 2018	Nov. 2019	-	\$14,578,036	-	\$14,578,036
061194	Mississippi Ave. – Perryville Rd. (Hwy. 10) (L.R.) (S)	10	8	Major Widening	Completed	Nov. 2014	May. 2016	0.70	\$12,966,800	0.70	\$12,966,800
061197*	I-30 S. Terminal Borrow Pond Access Rd. (S)			Safety Improvements	Completed		Oct. 2016	-	\$235,291	-	\$235,291
061202	Saline Co. Line – Otter Creek Rd. (Little Rock) (S)	5	9	Major Widening	Completed	Jun. 2011	Sep. 2014	1.27	\$12,646,682	1.49	\$14,837,447
	Addt'l Rte.-Sec.: Saline 5-8										

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061207	White Oak Bayou – I-40 (NLR) (F)	100	0	Major Widening	Programmed			1.08	\$5 - \$10 M	1.08	\$5 - \$10 M
061208*	Bluebird Ln. Prop. Release (Job 6873-1 Part of Tract 132) (S)			Right of Way	Programmed			-	-	-	-
061210*	Forest Park (Little Rock) SRTS E (2007)			Miscellaneous	Completed	Aug. 2008	Apr. 2014	-	\$5,196	-	\$5,196
061218	Union Pacific R.R. Viaduct Safety Impvts. (Little Rock) (S)	10	8	Safety Improvements	Completed	May. 2012	Apr. 2013	0.07	\$735,094	0.07	\$735,094
061223*	Arkansas River Trail Completion (S)			Enhancement	Completed	Oct. 2009	Jul. 2014	-	\$47,100	-	\$47,100
061244	I-430/I-630 Interchange Modifications (Phase III) (F) Addt'l Rte.-Sec.: Pulaski 630-21, CS	430	21	Interchange Improvements	Completed	Nov. 2010	Aug. 2015	-	\$103,379,526	-	\$103,379,526
061250	Hwys. 100/365 Roundabout (Pike Ave.) (NLR) (F)	100	1	Safety Improvements	Completed	Oct. 2009	Jul. 2014	-	\$1,330,279	-	\$1,330,279
061251*	Little Maumelle River Pedestrian/Bicycle Bridge (Pulaski Co.) (S)	New		Structure & Approaches	Completed	Nov. 2009	Jul. 2014	-	\$6,531,224	-	\$6,531,224
061255*	Little Maumelle River Str. & Apprs. (Kanis Rd.) (Pulaski Co.) (S)	CS		Reconstruction	Completed	May. 2016	May. 2017	-	\$1,804,403	-	\$1,804,403
061260*	I-630 Corridor Fixed Guideway Alignment Study	630	21	Study	Completed		Apr. 2016	-	\$194,925	-	\$194,925
061261*	Redmond Rd. – Cabot (Widening) P.E. Addt'l Rte.-Sec.: Lonoke 67-11	67	10	PE Only	Programmed			-	-	-	-
061264*	Motorized Trail Land Purchase (NLR) (S)			Roadside Appurtenances	Completed	Feb. 2012	Jul. 2014	-	\$362,124	-	\$362,124
061265*	Bayou Meto Creek Trail (Jacksonville) (S)			Enhancement	Completed	Aug. 2010	Sep. 2014	-	\$64,291	-	\$64,291
061266*	Odom Blvd. & Lake Willastein Trail (Maumelle) (S)			Enhancement	Completed	Aug. 2010	Sep. 2014	-	\$49,570	-	\$49,570
061267	W. Main St./Harris Rd./Jacksonville Cutoff Inters. Impvts. (Jacksonville) (S)	CS		Safety Improvements	Completed	Dec. 2013	Jul. 2014	-	\$936,570	-	\$936,570
061275	Arkansas River Str. & Apprs. (Broadway) (LR/NLR) (F)	70	12	Structure & Approaches	Completed	Sep. 2014	Sep. 2017	-	\$103,942,092	-	\$103,942,092
061276	Redmond Rd. & Main St. Strs. & Apprs. (Jacksonville) (F)	67	10	Structure & Approaches	Completed	Jun. 2014	May. 2018	1.25	\$47,747,595	1.25	\$47,747,595
061277	Union Pacific RR Str. & Apprs. (Roosevelt Rd.) (LR) (S)	70	12	Structure & Approaches	Completed	Dec. 2014	Jun. 2017	0.48	\$10,618,036	0.48	\$10,618,036
061288*	North Little Rock SRTS I (2010)			Miscellaneous	Completed		Jul. 2014	-	\$67,500	-	\$67,500
061294*	McCain Rail Grade Separation (NLR) (S)	CS		Structure & Approaches	Completed	Mar. 2016	Mar. 2018	-	\$10,173,454	-	\$10,173,454
061295*	Maryland Avenue Impvts. & Extension (Sherwood) (S)	CS		New Location	Under Construction	Sep. 2020		-	\$3,565,357	-	\$3,565,357
061296*	Levy UPRR Spur Bikeway (NLR) (S)			Enhancement	Completed		Dec. 2014	-	\$1,799,114	-	\$1,799,114
061300*	Main St. Viaduct (NLR) (S)	CS		Bridge Rehabilitation	Programmed			-	\$15 - \$20 M	-	\$15 - \$20 M
061301*	Maumelle Pedestrian/Bicycle Facilities (Phase II) (S)			Enhancement	Completed	Apr. 2013	Jul. 2014	-	\$492,331	-	\$492,331
061303*	Five Mile Creek Str. & Apprs. (Remount Rd.) (NLR) (S)	CS		Structure & Approaches	Completed	Nov. 2014	Jan. 2015	-	\$884,498	-	\$884,498
061313	Hwy. 176/Oakbrooke Dr. Signal (Sherwood) (S) Addt'l Rte.-Sec.: Pulaski CS	176	2	Safety Improvements	Completed	Feb. 2013	Oct. 2013	-	\$222,500	-	\$222,500
061322*	Jacksonville Marshall Rd. Sidewalks (ATEP-11) (S)			Enhancement	Completed	Feb. 2013	Jun. 2013	-	\$112,113	-	\$112,113
061323*	Maumelle Club Manor Dr. Sidewalks (ATEP-11) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
061324*	NLR Levy Spur Multi-use Trail (ATEP-11) (S)			Enhancement	Completed	Sep. 2012	Jan. 2013	-	\$542,130	-	\$542,130
061328	I-30 – I-40 (Sel. Secs.) (Cable Median Barrier) (S)	430	21	Safety Improvements	Completed	Jun. 2012	Nov. 2012	7.31	\$1,760,538	7.31	\$1,760,538
061331	Pleasant Ridge Rd. – Pleasant Valley Dr. (L.R.) (F)	10	8	Major Widening	Under Construction	Feb. 2020	<i>Early 2023</i>	2.12	\$81,049,325	2.12	\$81,049,325
061332	I-30/I-430 Interchange Impvt. (L.R.) (Ph. I) (S) Addt'l Rte.-Sec.: Pulaski 430-21	30	23	Major Widening	Completed	Jul. 2014	Apr. 2015	-	\$11,958,253	-	\$11,958,253
061333	I-430/Hwy. 10 Interchange Impvt. (L.R.) (S) Addt'l Rte.-Sec.: Pulaski 10-8	430	21	Interchange Improvements	Completed	Dec. 2016	Dec. 2017	-	\$22,892,896	-	\$22,892,896
061336*	145th Street R.R. Signals Upgrade (Wrightsville) (S)	CS		RR Crossing	Completed	Nov. 2011	Dec. 2012	-	\$161,478	-	\$161,478
061337*	Emerald Park Trail (Ph. II) (NLR) (S)			Enhancement	Completed	Apr. 2012	Jul. 2014	-	\$221,162	-	\$221,162
061338*	Sherwood City Hall Trail (S)			Enhancement	Completed	Apr. 2012	Jul. 2014	-	\$61,064	-	\$61,064
061342*	Hwy. 10 Improvements (LR) P.E.	10	8	PE Only	Programmed			-	-	-	-
061343	I-40 & Hwy. 270 Overhead Sign Structures Replacement (S)			Safety Improvements	Completed	Jun. 2012	Dec. 2012	-	\$93,666	-	\$212,877
061348	UPRR/Parkway Dr. Str. & Apprs. (S)	365	11	Structure & Approaches	Completed	Dec. 2015	Mar. 2018	0.40	\$8,990,100	0.40	\$8,990,100
061350*	Bayou Meto Spring Mitigation Bank (S)			Miscellaneous	Programmed			-	< \$1 M	-	< \$1 M
061363*	North Little Rock SRTS E (2011)			Miscellaneous	Completed	Apr. 2012	Aug. 2013	-	\$44,740	-	\$44,740
061364*	Pulaski Heights Elementary SRTS E (2011)			Miscellaneous	Completed	Feb. 2012	Aug. 2012	-	\$15,695	-	\$15,695
061366*	Pulaski Heights Elementary SRTS I (2011)			Miscellaneous	Completed	Jul. 2013	Jul. 2014	-	\$86,000	-	\$86,000
061367*	I-40/I-430 Interchange Modifications P.E. Addt'l Rte.-Sec.: Pulaski 430-21	40	33	PE Only	Programmed			-	\$10 - \$15 M	-	\$10 - \$15 M
061382	Taylor Loop Rd. – Pleasant Ridge Rd. (S)	10	8	Major Widening	Scheduled	Feb. 2025		2.31	\$20 - \$30 M	2.31	\$20 - \$30 M
061385*	Public Transportation Administration Facility (LR) (S)			Buildings	Completed	Jan. 2013	Aug. 2013	-	\$1,270,000	-	\$1,270,000
061386*	Hwy. 67 – I-40 West (North Belt Freeway Toll Feasibility Study)	New		Study	Completed		Nov. 2016	-	\$499,937	-	\$499,937
061390*	Crooked Creek Channel Impvts. (I-30) (S)	30	23	Miscellaneous	Completed	Jun. 2016	Feb. 2017	-	\$1,306,981	-	\$1,306,981
061394	Jacksonville – Lonoke Co. Line (T.P. White Rd.) (Overlay) (S)	67	10	Resurfacing	Completed	Apr. 2013	Aug. 2013	3.70	\$714,373	3.70	\$714,373
061399*	Levy Spur Trail Phase II (North Little Rock) (S)			Enhancement	Completed	Apr. 2014	May. 2015	-	\$86,316	-	\$86,316
061400*	Coleman Creek Greenway Extension (UALR) (S)			Enhancement	Completed	Mar. 2014	May. 2015	-	\$34,960	-	\$34,960
061401*	Rock Creek Trail Extension (Little Rock) (S)			Enhancement	Completed	Jun. 2014	Dec. 2016	-	\$50,000	-	\$50,000
061402*	Green Valley Trail (Sherwood) (S)			Enhancement	Completed	Sep. 2014	Apr. 2016	-	\$38,600	-	\$38,600
061407	Geyer Springs Rd. – 65th St. (Pavement Friction Impvts.) (S)	30	23	Safety Improvements	Completed	Jul. 2013	Oct. 2013	2.56	\$1,150,280	2.56	\$1,150,280
061408	Hwy. 165 – Faulkner Lake Rd. (Pavement Friction Impvts.) (S)	440	1	Safety Improvements	Completed	Sep. 2013	Nov. 2013	1.00	\$146,473	1.00	\$146,473
061412*	Jacksonville SRTS I (2012)			Miscellaneous	Completed	Nov. 2016	Sep. 2017	-	\$140,087	-	\$140,087

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061414*	North Little Rock SRTS I (2012)			Miscellaneous	Completed	Jan. 2018	Dec. 2018	-	\$90,902	-	\$90,902
061415*	North Little Rock SRTS E (2012)			Miscellaneous	Completed		Jun. 2016	-	\$44,207	-	\$44,207
061416*	Univ. Dist. Dev. Corp. & Little Rock SRTS I (2012)			Roadside Appurtenances	Completed	Apr. 2018	Jun. 2019	-	\$121,311	-	\$121,311
061417*	Sherwood SRTS I (2012)			Miscellaneous	Completed	Aug. 2015	Jun. 2016	-	\$91,991	-	\$91,991
061420*	NLR Shilcott Bayou Multi-Use Bridge (S)	CS		Structure & Approaches	Completed	Nov. 2013	Aug. 2014	-	\$743,985	-	\$743,985
061421*	Public Trans. Admin. Facility (Parking & Receiving) (LR) (S)	New		Buildings	Completed	Apr. 2014	Dec. 2014	-	\$772	-	\$772
061422*	Little Rock Bike Connector (Phase 2) (S)	CS		Enhancement	Completed	Apr. 2015	Jun. 2022	-	\$737,500	-	\$737,500
061423	N. Cantrell Rd. Str. & Apprs. (Little Rock) (S)	CS		Structure & Approaches	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061424	Hwy. 67 Interim Pvmnt. Impvts. (Jacksonville-Cabot) (S) Addt'l Rte.-Sec.: Lonoke 67-11	67	10	Rehabilitation	Completed	Jun. 2014	Mar. 2015	5.98	\$2,549,608	6.69	\$2,864,728
061430	I-430 – West (Overlay) (S)	100	0	Resurfacing	Completed	Apr. 2014	Sep. 2014	6.18	\$2,164,432	6.18	\$2,164,432
061433*	Marche Rd. RR Signal (East of Maumelle) (S)			RR Crossing	Completed	Oct. 2014	Aug. 2015	-	\$147,633	-	\$147,633
061434*	Military Rd. RR Sig. Upgrade & Traffic Sig. (NLR) (S)	CS		RR Crossing	Completed	Jul. 2017	Aug. 2018	-	\$642,764	-	\$642,764
061435*	Ott Park Trail (Ph. I) (North Little Rock) (RTP-14) (S)			Enhancement	Completed	Jul. 2015	Mar. 2016	-	\$139,412	-	\$139,412
061436*	Central Office Building Improvements (S)			Buildings	Under Construction	Jul. 2017		-	\$0	-	\$0
061437	I-30/I-430 Interchange Impvt. (L.R.) (Ph. II) (S) Addt'l Rte.-Sec.: Pulaski 430-21	30	23	Major Widening	Completed	Dec. 2015	Nov. 2016	-	\$25,086,141	-	\$25,086,141
061444*	Benton – South Terminal Interchange (I-30 Corridor Study) (S) Addt'l Rte.-Sec.: Saline 30-23	30	22	Study	Completed	Jan. 2020	Mar. 2020	21.57	\$781,252	21.57	\$781,615
061448	Pulaski Co. Area 1 Headquarters/R.E. Office 61 (S)	70	13	Buildings	Completed	Jul. 2018	Sep. 2019	-	\$1,934,023	-	\$1,934,023
061452*	Lucky Dr. RR Signals (SW of Jacksonville) (S)			RR Crossing	Completed	Dec. 2015	Jun. 2018	-	\$405,365	-	\$405,365
061454	Gill St. & RR Overpass Strs. & Apprs. (S)	10	8	Structure & Approaches	Scheduled	Nov. 2022		0.39	\$15 - \$20 M	0.39	\$15 - \$20 M
061458*	W. 24th St. RR Signals Upgrade (NLR) (S)			RR Crossing	Completed		Jan. 2020	-	\$179,035	-	\$179,035
061459*	Hwy. 70 RR Signals Upgrade (NLR) (S)			RR Crossing	Programmed			-	< \$1 M	-	< \$1 M
061465	I-30 – South (Overlay) (S) Addt'l Rte.-Sec.: Saline 111-3	111	2	Resurfacing	Completed	Mar. 2016	Aug. 2016	0.84	\$137,684	1.89	\$309,789
061468	University Ave. Traffic Ops. Impvts. (Little Rock) (S)	70	12	Safety Improvements	Under Construction	Jul. 2019		-	\$2,093,369	-	\$2,093,369
061469	Hwys. 100 & 365 Traffic Ops. Impvts. (Pulaski Co./Maumelle/NLR) (S) Addt'l Rte.-Sec.: Pulaski 365-11	100	0	Safety Improvements	Completed	May. 2019	Jun. 2020	7.89	\$260,489	7.89	\$260,489
061472	Hwy. 161 Str. & Apprs. (Pulaski & Lonoke Cos.) (S) Addt'l Rte.-Sec.: Lonoke 161-5	161	5	Structure & Approaches	Scheduled	Aug. 2022		0.11	\$1 - \$3 M	0.22	\$3 - \$5 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061476*	Wetland Trail (Maumelle) (RTP-15) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061477*	Levy Trail (Ph. 3) (North Little Rock) (RTP-15) (S)			Enhancement	Completed	Nov. 2018	Jun. 2020	-	\$320,345	-	\$320,345
061481*	MacPark Connections (Little Rock) (SRTS-15) (S)			Enhancement	Completed	May. 2019	May. 2020	-	\$6,626	-	\$6,626
061488*	Rock Region Metro Bus Shelters (Pulaski Co.) (TAP-15) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061489*	N. 1st St. Sidewalk (Jacksonville) (TAP-15) (S)			Enhancement	Completed	Aug. 2018	Jul. 2019	-	\$110,893	-	\$110,893
061490*	AR River Trail Riverfront Dr. (Little Rock) (TAP-15) (S)			Enhancement	Completed	Aug. 2018	Oct. 2020	-	\$194,639	-	\$194,639
061491*	Dunbar/Gibbs School Sidewalks (Little Rock) (TAP-15) (S)			Enhancement	Completed	Aug. 2017	Nov. 2019	-	\$149,754	-	\$149,754
061492*	Amboy/Boone School Sidewalks (N. Little Rock) (TAP-15) (S)			Enhancement	Under Construction	May. 2022		1.48	\$147,890	1.48	\$147,890
061493*	Raywood – Autumnbrook Sidewalks (Sherwood) (TAP-15) (S)			Enhancement	Under Construction	Apr. 2018		-	\$113,900	-	\$113,900
061494*	AR River Trail Pinnacle Valley Rd. (Pulaski Co.) (TAP-15) (S)			Enhancement	Completed	Nov. 2018	Aug. 2020	-	\$1,336,249	-	\$1,336,249
061495*	Shorter College Streetscape (TAP-15) (S)			Enhancement	Completed	Apr. 2017	Mar. 2020	-	\$538,467	-	\$538,467
061499*	W. 18th St. RR Signals Upgrade (NLR) (S)	CS		RR Crossing	Completed	Sep. 2016	Jan. 2020	-	\$211,347	-	\$211,347
061503	I-630 – Markham St. (Little Rock) (Mill & Inlay) (S)	70	12	Resurfacing	Completed	Aug. 2016	Sep. 2016	0.62	\$315,451	0.62	\$315,451
061504*	Perryville Rd. – Kavanaugh Blvd. (L.R.) (Hwy. 10 Study) (S)	10	8	Study	Programmed			-	< \$1 M	-	< \$1 M
061505*	I-30 – I-630 Bridge Painting (I-430) (S)	430	21	Miscellaneous	Completed	Nov. 2016	Jun. 2017	-	\$1,179,631	-	\$1,179,631
061506	Shilcotts Bayou Str. & Apprs. (North Little Rock) (S)	176	1	Structure & Approaches	Completed	Apr. 2020	Nov. 2020	0.08	\$1,235,329	0.08	\$1,235,329
061507	Palarm Creek Str. & Apprs. (S)	365	11	Structure & Approaches	Sub. Completed	Jun. 2020	Feb. 2022	0.33	\$3,837,971	0.33	\$3,837,971
061510	Hwy. 70/University Ave. Inters. Impvts. (S)	70	12	Safety Improvements	Scheduled	May. 2023		-	\$1 - \$3 M	-	\$1 - \$3 M
061515	Hwy. 365 – Hwy. 70 (North Little Rock) (S)	100	1	Resurfacing	Completed	May. 2017	Nov. 2017	1.54	\$652,907	1.54	\$652,907
061518	Hwy. 5 – Mabelvale Pike (S)	338	1	Resurfacing	Completed	Feb. 2017	Jun. 2017	1.90	\$392,800	1.90	\$392,800
061521	Fourche Creek – Hwy. 70 (S)	367	13	Resurfacing	Completed	Feb. 2017	Jun. 2017	1.13	\$228,348	1.13	\$228,348
061522	Hwy. 161 – Lonoke Co. Line (S)	294	1	Resurfacing	Completed	Jan. 2017	Nov. 2017	2.30	\$378,769	2.30	\$378,769
061525	Hwy. 165 – Lonoke Co. Line (S)	70	13	Resurfacing	Completed	Feb. 2017	Aug. 2017	8.97	\$1,822,716	8.97	\$1,822,716
061526*	Main St. & Roosevelt Rd. Sidewalks (LR) (S)			Enhancement	Completed	Jun. 2018	Jul. 2019	-	\$152,632	-	\$152,632
061527*	JP Wright Loop Rd. Rail Grade Separation (S)	CS		RR Crossing	Scheduled	2022		-	\$5 - \$10 M	-	\$5 - \$10 M
061531	Landski Dr. – Pershing Blvd. (North Little Rock) (S)	365	11	Resurfacing	Completed	Oct. 2016	Nov. 2016	1.66	\$483,444	1.66	\$483,444
061532*	Sherwood Indianhead Walking Trail (RTP-16) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061538*	Jacksonville Military Rd. Sidewalks (TAP-16) (S)			Enhancement	Completed	Aug. 2019	Aug. 2020	0.40	\$468,750	0.40	\$468,750
061539*	Little Rock Zoo Trails (TAP-16) (S)			Enhancement	Completed	Jun. 2019	Jun. 2021	0.76	\$776,423	0.76	\$776,423
061540*	NLR Bishop Lindsey Streetscape (TAP-16) (S)			Enhancement	Completed	Jun. 2019	Jan. 2021	-	\$493,780	-	\$493,780
061545*	Edgewood Dr. Sidewalks (Maumelle) (S)			Enhancement	Completed	Aug. 2018	Oct. 2021	-	\$218,100	-	\$218,100
061550*	Pulaski Co. AR River Trail Pinnacle Valley Rd. Ph. 2 (TAP-16) (S)			Enhancement	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061551	Pike Ave. Bike/Ped. Impvts. (NLR) (S)	365	11	Safety Improvements	Under Construction	Dec. 2021		0.53	\$569,380	0.53	\$569,380
061552*	12th St. Jump Start Impvts. (Little Rock) (S)	CS		Miscellaneous	Under Construction	Jun. 2020		-	\$2,032,775	-	\$2,032,775
061553*	Park Hill Community Jump Start Impvts. (NLR) (S)	New		Miscellaneous	Under Construction	Aug. 2021		-	\$4,775,551	-	\$4,775,551
061554*	Levy Community Jump Start Impvts. (NLR) (S)	New		Miscellaneous	Under Construction	Oct. 2020		-	\$1,957,136	-	\$1,957,136
061556*	Kelso Rd. & Burns Trail Sidewalks (Sherwood) (S)	New		Enhancement	Completed	Jun. 2018	Nov. 2019	-	\$191,220	-	\$191,220
061559*	Hwy. 365 RR Signal Upgrade (Woodson) (S)	365	12	RR Crossing	Completed	Apr. 2018	Dec. 2021	-	\$111,062	-	\$111,062
061562*	Southwest Trail Design Addt'l Rte.-Sec.: Garland New; Saline New	New		Enhancement	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061565*	Jacksonville Pinewood Elem. Sidewalks (TAP-17) (S)			Enhancement	Completed	Jun. 2018	Oct. 2018	-	\$154,020	-	\$154,020
061566*	North Little Rock Recycle Bikes for Kids NI (TAP-17) (S)			Enhancement	Completed		Jun. 2022	-	\$19,275	-	\$19,275
061568*	ADPHT Pinnacle Mt. State Park Shared-Use Path (RTP-17) (S)	New		Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061569*	Little Rock Ottenheimer Accessibility Trail (RTP-17) (S)			Enhancement	Completed	May. 2019	Nov. 2019	-	\$83,180	-	\$83,180
061570*	UALR Coleman Creek Greenway Ext. (RTP-17) (S)	New		Enhancement	Completed	Nov. 2018	Aug. 2019	-	\$60,000	-	\$60,000
061572*	Vimy Ridge Rd./County Line Rd. Inters. Impvts. (Shannon Hills) (S)			Safety Improvements	Under Construction	Jan. 2020		-	\$151,717	-	\$303,435
061580*	Oneida St. Bridge Replacement (Pulaski Co.) (S)	New		Structure & Approaches	Under Construction	Mar. 2020		-	\$1,052,471	-	\$1,052,471
061582	Brodie Creek – Hwy. 70 (Little Rock) (S)	5	9	Resurfacing	Completed	Jan. 2021	Apr. 2021	2.57	\$1,124,740	2.57	\$1,124,740
061589	Hwy. 67 – Hwy. 440 (Jacksonville) (S)	161	3	Resurfacing	Completed	Jun. 2020	Nov. 2020	5.46	\$1,661,678	5.46	\$1,661,678
061590	I-40 – S. Redmond Rd. (S)	67	10	Resurfacing	Scheduled	2025		8.39	\$3 - \$5 M	8.39	\$3 - \$5 M
061596	North Hills Blvd. – Stonehenge Dr. (Sherwood) (S)	107	1	Resurfacing	Completed	May. 2020	Nov. 2020	6.04	\$2,112,736	6.04	\$2,112,736
061597	Reservoir Rd. – Mississippi Ave. (Little Rock) (S)	10	8	Resurfacing	Completed	Jun. 2020	Oct. 2020	1.22	\$563,806	1.22	\$563,806
061602	Hwy. 391 – Hwy. 70 (North Little Rock) (S)	165	9	Resurfacing	Completed	Apr. 2019	Jun. 2019	5.19	\$2,004,691	5.19	\$2,004,691
061605*	ADPHT Pinnacle Mtn. Park – Ouachita Trail Rehab. (RTP-18) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061612	I-530 – Hwy. 67 (Widening & Reconst.) (I-30 & I-40) P.E. Addt'l Rte.-Sec.: Pulaski 40-33	30	23	Major Widening	Programmed			7.22	-	7.22	-
061616*	Allsopp Park Trail Connection (Little Rock) (S)			Enhancement	Completed	Feb. 2020	Sep. 2020	-	\$200,000	-	\$200,000
061618*	LR Port Authority Transit Shelter (S)	New		Miscellaneous	Completed	Nov. 2019	Aug. 2020	-	\$57,672	-	\$57,672
061622	Sevier St. – Geyer Springs Rd. (Conc. Pvmnt. Pres.) (S) Addt'l Rte.-Sec.: Saline 30-22	30	23	Resurface & Shoulder	Under Construction	Feb. 2022	Late 2023	6.38	\$15,472,324	16.72	\$40,548,158
061623*	Little Rock Central High Corridor Ph. 1 (S)	New		Miscellaneous	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061624*	Fairway Park Trail (Sherwood) (S)			Miscellaneous	Scheduled	2022		-	< \$1 M	-	< \$1 M
061625*	General Samuels Rd. – Republican Rd. (Hwy. 107 Study) (S)	107	1	Study	Completed		Oct. 2021	4.89	\$150,351	4.89	\$150,351

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061630	Hwy. 10 – Hwy. 100 (System Preservation & ITS Impvts.) (S)	430	21	Bridge Rehabilitation	Under Construction	Jun. 2020	Jul. 2022	2.37	\$31,722,871	2.37	\$31,722,871
061636*	North Little Rock 14th St. Ped. Bridge (TAP-19) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061637*	Pulaski Co. Two Rivers Park Safety Impvts. (TAP-19) (S)			Enhancement	Completed	Jul. 2020	Apr. 2021	-	\$268,565	-	\$268,565
061639*	Little Rock Boyle Park Bike Trails (RTP-19) (S)			Enhancement	Under Construction	Apr. 2021		1.68	\$125,420	1.68	\$125,420
061640*	ARDOT Central Office Property Acquisition			Buildings	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061641*	E. Hensley Rd. RR Signals (Hensley) (S)	CS		Safety Improvements	Programmed			-	< \$1 M	-	< \$1 M
061643*	District 6 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	107	1	Sealing	Programmed			10.50	< \$1 M	69.72	\$1 - \$3 M
061646	South St. – I-430 (Frontage Rd.) (S) Addt'l Rte.-Sec.: Saline 30-22	30	23	Resurfacing	Scheduled	Feb. 2023		4.85	\$1 - \$3 M	26.76	\$5 - \$10 M
061650*	ADPHT Pinnacle Mountain Shared-Use Path (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061654*	Central High School Safety Impvts. (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061655*	SW Trail: Saline Co. – Geyer Springs Rd. (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061663*	Rock Region METRO Supershelters (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061666	Cabot – Hwy. 107 (S) Addt'l Rte.-Sec.: Lonoke 89-1	89	2	Resurfacing	Scheduled	2024		4.32	\$1 - \$3 M	6.26	\$1 - \$3 M
061669	Goodson Rd. – Chenal Pkwy. (Little Rock) (S) Addt'l Rte.-Sec.: Pulaski 10-8	10	7	Resurfacing	Scheduled	Apr. 2023		2.52	\$1 - \$3 M	2.52	\$1 - \$3 M
061670	Chenal Pkwy. – Taylor Loop Rd. (Little Rock) (S)	10	8	Resurfacing	Scheduled	Apr. 2023		2.80	\$1 - \$3 M	2.80	\$1 - \$3 M
061672	I-40 – McCain Blvd. (NLR) (Sel. Secs.) (S)	107	1	Resurfacing	Scheduled	2024		0.86	< \$1 M	0.86	< \$1 M
061673*	LR Two Rivers Park Trail Rehab. (RTP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061676	Colonel Maynard Rd. – I-440 (NLR) (S)	165	9	Major Widening	Programmed			2.99	\$20 - \$30 M	2.99	\$20 - \$30 M
061677	I-440 – Kerr Rd. (S) Addt'l Rte.-Sec.: Lonoke 40-41	40	33	Major Widening Safety Improvements	Programmed			5.43	\$50 - \$75 M	6.79	\$75 - \$100 M
061679*	Pike Ave. Impvts. (NLR) (S)	365	11	Safety Improvements	Programmed			0.69	\$3 - \$5 M	0.69	\$3 - \$5 M
061683	Geyer Springs Rd. – 65th St. (F)	30	23	Resurfacing	Programmed			2.69	\$20 - \$30 M	2.69	\$20 - \$30 M
061684	Hwy. 67 – Hwy. 161 (F)	40	33	Reconstruction	Programmed			1.50	\$10 - \$15 M	1.50	\$10 - \$15 M
061685	Hwy. 161 – Hwy. 31 (S) Addt'l Rte.-Sec.: Lonoke 40-41	40	33	Resurfacing	Sub. Completed	Jun. 2021	Jun. 2022	7.43	\$7,260,271	18.60	\$18,175,108
061689	I-30 – Cross St. (F)	630	21	Reconstruction	Programmed			1.80	\$3 - \$5 M	1.80	\$3 - \$5 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061690	Cross St. – Dennison St. (F)	630	21	Reconstruction	Programmed			0.73	\$1 - \$3 M	0.73	\$1 - \$3 M
061691	Dennison St. – Cedar St. (F)	630	21	Rehabilitation	Programmed			0.98	\$1 - \$3 M	0.98	\$1 - \$3 M
061692	65th St. – South Terminal (Reconst.) (S)	30	23	Reconstruction	Programmed			2.18	\$175 - \$200 M	2.18	\$175 - \$200 M
061693*	Bowman Rd./Kanis Rd. Impvts. (Little Rock) (S)	CS		Major Widening	Under Construction	Apr. 2022		-	\$4,794,265	-	\$4,794,265
061694*	CARTS Accessibility Standards (Metroplan) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061695*	CARTS Regional Trails Master Plan (Metroplan) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061696*	Southeast Trail (Pulaski Co.) (S)	New		Enhancement	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061700*	Argenta Plaza Streetscaping (NLR) (S)	New		Enhancement	Under Construction	Feb. 2022		-	\$269,000	-	\$269,000
061702*	Coolhurst Sidewalks (Sherwood) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061706	I-440/Fourche Dam Pike Intchg. Impvts. (Little Rock) (S)	440	1	Safety Improvements	Under Construction	May. 2021		-	\$884,936	-	\$884,936
061709*	Overhead Sign Strs. & Signs Replacement (Central AR) (S) Addt'l Rte.-Sec.: Garland 70-9, 270-5/6; Pulaski 440-2; Saline 30-22	30	23	Safety Improvements	Under Construction	May. 2021	Mid 2023	-	\$420,078	-	\$1,680,308
061710	Fairfax Dr. – Hwy. 70 (NLR) (S)	161	3	Resurfacing	Completed	Aug. 2021	Nov. 2021	1.70	\$735,334	1.70	\$735,334
061711*	Highway 176Y Scoping Study (S)	176	2	Safety Improvements	Programmed			-	-	-	-
061712*	Kanis Rd./Denny Rd./Stewart Rd. Roundabout (Pulaski Co.) (S)	CS		Safety Improvements	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061713*	Power-Line Trail (Sherwood) (S)	CS		Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061714*	Tri-Creek Greenway Ph. III (Little Rock) (S)			Enhancement	Programmed			-	\$3 - \$5 M	-	\$3 - \$5 M
061715*	W. Main St. Realignment (Jacksonville) (S)	CS		Reconstruction	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061716*	White Oak Crossing Roundabout (Mauvelle) (S)	CS		Safety Improvements	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061722	Hwy. 70/Hwy. 391 Impvts. (North Little Rock) (S) Addt'l Rte.-Sec.: Pulaski 391-1	70	13	Major Widening Safety Improvements	Completed	Mar. 2021	Oct. 2021	0.69	\$2,489,145	0.69	\$2,489,145
061724*	Jacksonville Military Rd. Sidewalks Ph. 2 (TAP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061725*	North Little Rock Recycle Bikes for Kids Ph. 2 NI (TAP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061726*	Shorter College Streetscaping (TAP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061730*	Little Rock Allsopp Park Multi-Use Trails (RTP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061731*	North Little Rock Ott Park Off-Road Trail Impvts. (RTP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061732*	Southwest Trail: Chicot Rd. – Geyer Springs Rd. (Pulaski Co.) (RTP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061733*	Ranch North Woods Trail (RTP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061734*	UALR Coleman Creek Greenway Ext. (RTP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061736*	Central Office Walking Trail Impvts. (RTP) (S)			Enhancement	Under Construction	Jan. 2022	Jul. 2022	-	\$107,490	-	\$107,490

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or Sub. Comp.</i> Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061738	General Samuels Rd. – Arnold Dr. (Sherwood) (S)	107	1	Major Widening	Scheduled	May. 2025		1.20	\$10 - \$15 M	1.20	\$10 - \$15 M
061747	Hwy. 176 – Hwy. 67 (Sherwood) (S)	176	2	Minor Widening	Scheduled	Sep. 2024		0.40	\$1 - \$3 M	0.40	\$1 - \$3 M
061752*	District 6 Headquarters (Little Rock) (S)	338	0	Buildings	Programmed			-	\$20 - \$30 M	-	\$20 - \$30 M
061753	Hwy. 440 – Fairfax Dr. (S)	161	3	Resurfacing	Programmed			4.03	\$1 - \$3 M	4.03	\$1 - \$3 M
061754*	Overhead Sign Strs. & Signs Replacement (Central AR) (2022) (S) Addt'l Rte.-Sec.: Hot Spring 30-21; Pulaski 440-1; Saline 30-22	30	23	Safety Improvements	Scheduled	Sep. 2022		-	< \$1 M	-	\$1 - \$3 M
061757*	Jonesboro Dr. Children's Trail (Little Rock) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061761	Bingham Rd. – Grant Co. Line (S) Addt'l Rte.-Sec.: Pulaski 530-3; Saline 530-2	530	1	Resurfacing	Programmed			4.02	\$1 - \$3 M	7.32	\$5 - \$10 M
061762*	Frazier Pike Railroad Signals Upgrade (Little Rock) (S)	CS		RR Crossing	Programmed			-	< \$1 M	-	< \$1 M
061763*	ARDOT Central Office Properties Modifications (S)	30	23	Buildings	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
A60001	I-30 – Roosevelt Rd. (Little Rock) (S)	70	12	Resurfacing	Completed	Apr. 2020	Jul. 2020	4.31	\$2,570,262	4.31	\$2,570,262
A60007*	District 6 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	10	7	Resurfacing	Completed		Jun. 2022	7.73	\$251,813	49.36	\$1,159,267
A60009	Hwy. 107 – Hwy. 67 (Sherwood) (S)	176	2	Resurfacing	Under Construction	Feb. 2022	Late 2022	2.96	\$590,244	2.96	\$590,244
A60010	Hwy. 70 – E. Roosevelt Rd. (Little Rock) (S)	365	12	Resurfacing	Under Construction	Apr. 2022	Late 2022	1.15	\$621,645	1.15	\$621,645
A60012	I-30 – Hwy. 367 (Little Rock) (S)	338	1	Resurfacing	Under Construction	May. 2022	Late 2022	4.03	\$2,859,259	4.03	\$2,859,259
A60016	East of I-40 – Military Dr. (S)	365	11	Resurfacing	Scheduled	Nov. 2022		7.57	\$3 - \$5 M	7.57	\$3 - \$5 M
A60019	Hwy. 440 Preservation Treatment (S)	440	2	Rehabilitation	Programmed			3.75	< \$1 M	3.75	< \$1 M
BB0611	Bankhead Dr. – Ark. River Bridge (S)	440	1	Reconstruction	Completed	Jan. 2016	Oct. 2016	2.82	\$34,413,308	2.82	\$34,413,308
BB0612	Ark. River Bridge – I-40 (S)	440	1	Reconstruction	Completed	Dec. 2016	Jun. 2018	3.29	\$43,273,835	3.29	\$43,273,835
BB0613	I-30 – Bingham Rd. (S) Addt'l Rte.-Sec.: Pulaski 530-1	530	0	Rehabilitation	Completed	Jul. 2014	Sep. 2015	8.19	\$65,144,703	8.19	\$65,144,703
BB0614	Bingham Rd. – Grant Co. Line (S) Addt'l Rte.-Sec.: Pulaski 530-3; Saline 530-2	530	1	Resurfacing	Completed	Nov. 2012	Aug. 2014	4.20	\$8,042,291	7.49	\$14,342,087
BB0618	I-430/Rodney Parham Rd. Intchnng. Impvts. (S)	430	21	Interchange Improvements	Completed	Jun. 2018	Nov. 2018	0.34	\$3,156,142	0.34	\$3,156,142
BB0620	Hwy. 391 Intchnng. Impvts. (S)	40	33	Interchange Improvements	Completed	Aug. 2017	Jul. 2018	1.18	\$9,398,176	1.18	\$9,398,176
BB0621	65th St. – South Terminal (Pvmt. Impvts.) (S)	30	23	Resurfacing	Completed	Nov. 2016	May. 2017	2.18	\$2,262,188	2.18	\$2,262,188
C60001*	Little Rock Main St Olay & Strpng(sel Sec)(s)	CS		Resurfacing	Completed	Sep. 2013	Dec. 2013	0.92	\$386,552	0.92	\$386,552
C60002*	Jacksonville James& 1st Sts Olay(sel Secs)(s)	CS		Resurfacing	Completed	Jun. 2014	Aug. 2014	1.45	\$273,934	1.45	\$273,934
C60003*	No Little Rock McCain Blvd Olay(sel Secs) (S)	CS		Resurfacing	Completed	Apr. 2014	Jun. 2014	0.91	\$299,305	0.91	\$299,305

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
C60004*	Sherwood Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jun. 2015	Sep. 2015	3.23	\$337,456	3.23	\$337,456
C60005*	Wrightsville Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Feb. 2018	Apr. 2018	1.29	\$236,018	1.29	\$236,018
C60006*	Jacksonville Main St & James St Ovrly(selsecs	CS		Resurfacing	Completed	May. 2018	Sep. 2018	0.80	\$191,231	0.80	\$191,231
C60007*	Nlr Lynch Dr & Flkner Lk Rd Ovrly (Selsec)(s	CS		Resurfacing	Completed	Apr. 2018	Oct. 2018	2.48	\$302,794	2.48	\$302,794
C60008*	Sherwood Overlay No.2 (Sel. Secs) (S)	CS		Resurfacing	Completed	Jul. 2019	Oct. 2019	1.78	\$341,371	1.78	\$341,371
C60009*	Cammack Village Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Feb. 2019	Jul. 2019	1.24	\$260,893	1.24	\$260,893
C60010*	Wrightsville Overlay & Surfacing (S)	CS		Resurfacing	Completed	Apr. 2021	Oct. 2021	1.02	\$267,509	1.02	\$267,509
C60011*	Little Rock 9th St. Overlay (Sel. Sec.) (S)	CS		Resurfacing	Completed	Jun. 2019	Dec. 2019	0.51	\$294,052	0.51	\$294,052
C60012*	Maumelle N. Odom Blvd. Overlay (S)	CS		Resurfacing	Completed	May. 2020	Sep. 2020	0.76	\$288,968	0.76	\$288,968
C76015*	Cabot & Maumelle Overlay (S) Addt'l Rte.-Sec.: Lonoke CS	CS		Resurfacing	Completed	Sep. 2014	Dec. 2014	1.31	\$363,299	6.69	\$991,896
C76057*	Alexander Overlay No. 2 (S) Addt'l Rte.-Sec.: Saline CS	CS		Resurfacing	Completed	Jan. 2020	May. 2020	0.21	\$153,208	1.79	\$306,417
CA0602	I-530 – Hwy. 67 (Widening & Reconst.) (I-30 & I-40) (F) Addt'l Rte.-Sec.: Pulaski 40-33	30	23	Major Widening Reconstruction Structure & Approaches	Under Construction	Mar. 2019	Early 2025	7.37	\$631,700,000	7.37	\$631,700,000
CA0603*	Hwy. 365 – I-430 (Widening) P.E.	40	33	PE Only	Programmed			-	-	-	-
CA0604	Main St. – Vandenberg Blvd. (Widening) (Jacksonville) (F)	67	10	Interchange Improvements Major Widening	Scheduled	Sep. 2022		1.99	\$125 - \$150 M	1.99	\$125 - \$150 M
CA0605	Vandenberg Blvd. – Hwy. 5 (Widening) (S) Addt'l Rte.-Sec.: Lonoke 67-11	67	10	Major Widening	Completed	Dec. 2016	May. 2019	4.06	\$69,752,652	4.60	\$79,264,377
CA0608	Baptist Hospital – University Ave. (Widening) (F)	630	21	Major Widening	Completed	Apr. 2018	Mar. 2020	2.16	\$87,384,772	2.16	\$87,384,772
CA0609	Hwy. 365 – I-430 (Widening) & I-430 Intchn. Mod. (F) Addt'l Rte.-Sec.: Pulaski 430-21	40	33	Interchange Improvements Major Widening	Completed	Sep. 2014	Apr. 2016	5.11	\$38,362,866	5.11	\$38,362,866
CA0613*	Jacksonville – Cabot (Widening & Intchn. Impvts.) (Sel. Secs.) P.E. Addt'l Rte.-Sec.: Lonoke 67-11	67	10	PE Only	Programmed			1.99	-	5.23	-
GF0657*	Sleepy Hollow Access (Lake Maumelle)boat Dock			Miscellaneous	Completed	Nov. 2016	Dec. 2016	-	\$4,900	-	\$4,900
GF0658*	Benny Craig Prk Accss(fourche Creek)boat Ramp			Miscellaneous	Completed	Jul. 2016	Apr. 2017	-	\$51,915	-	\$51,915
R60101*	Hwy. 67 – I-40 West P.E.	440	3	PE Only	Programmed			-	-	-	-
SA6046*	Pulaski County Surfacing No. 8(SEL. Secs.)(s)	CR		Resurfacing	Completed	Jul. 2014	Oct. 2014	3.13	\$346,521	3.13	\$346,521

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PULASKI COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
SA6047*	Pulaski County Surfacing No 9(SEL. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2015	Nov. 2015	6.09	\$697,933	6.09	\$697,933
SA6048*	Jacksonville-Cato Rd.-Watson Rd. (Olay) (S)	CR		Resurfacing	Completed	Aug. 2016	Nov. 2016	2.15	\$189,163	2.15	\$189,163
SA6049*	Pulaski Co. Surfacing No. 10 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2017	Dec. 2017	3.43	\$422,508	3.43	\$422,508
SA6050*	Pulaski County Overlay No.4 (S)	CR		Resurfacing	Completed	Jun. 2019	Sep. 2019	2.13	\$412,785	2.13	\$412,785
SA6051*	Pulaski County Overlay No. 5 (S)	CR		Resurfacing	Completed	May. 2020	Aug. 2020	3.97	\$603,150	3.97	\$603,150
SA6052*	Lawson Rd. Overlay (S)	CR		Resurfacing	Completed	Jun. 2021	Nov. 2021	1.40	\$235,789	1.40	\$235,789
SA6053*	Pulaski Co. Seal & Microsurface (S)	CR		Resurfacing	Completed	Jun. 2021	Oct. 2021	4.87	\$380,697	4.87	\$380,697
Totals For All Projects In Pulaski County								330.57	\$1,923,243,625		

* Job not shown on county map.
