


Crawford County

District 4 Job Status Map

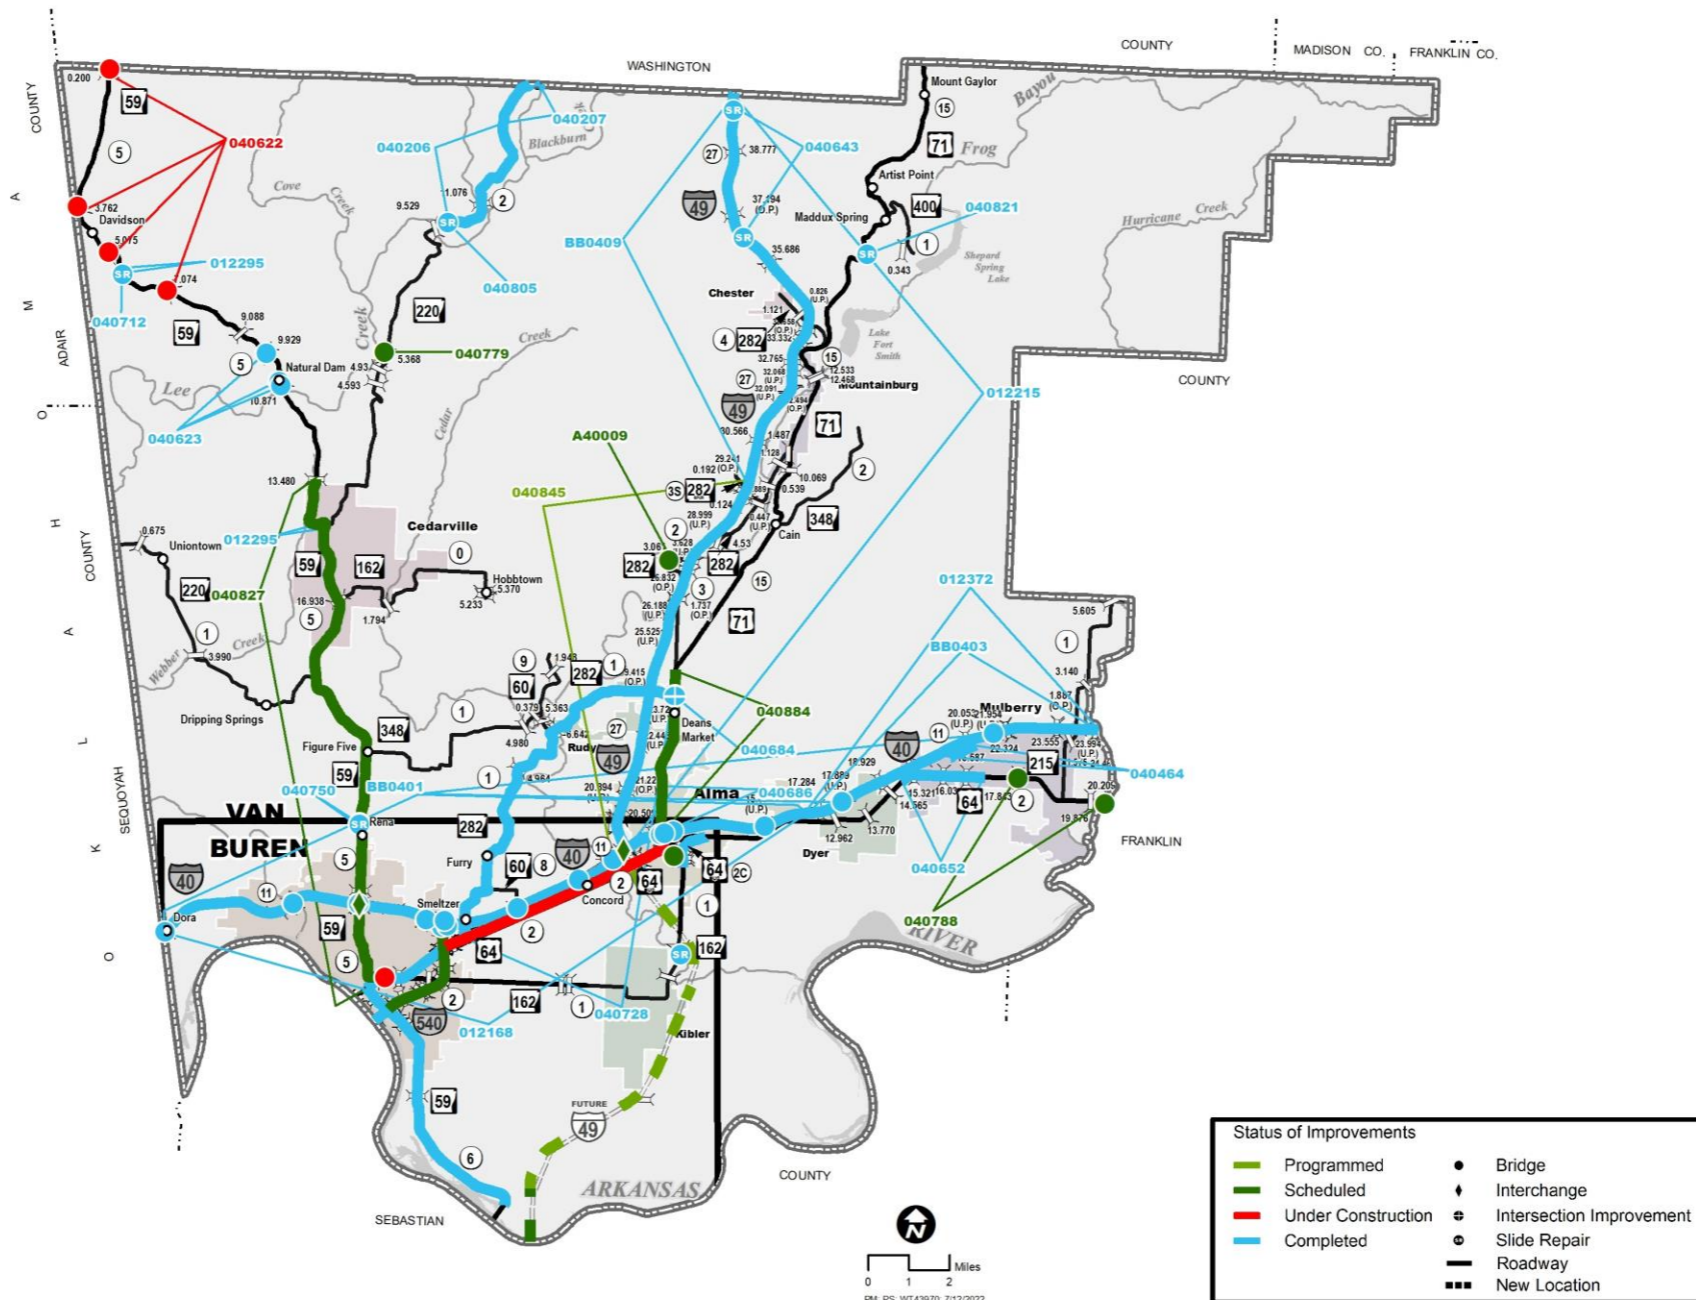

SUMMARY OF CONSTRUCTION PROJECTS

CRAWFORD COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
001725*	Oklahoma Line – North Terminal P.E. Addt'l Rte.-Sec.: Various	40	11	PE Only	Completed		Aug. 2021	-	\$2,296,302	-	\$2,296,302
001852*	Oht Trails Maintenance (S) Addt'l Rte.-Sec.: Various			Enhancement	Completed	Jan. 2000	Mar. 2015	-	\$6,200	-	\$31,000
004825*	Crawford & Seb Co Contr Jt Rehab(sel Rts&secs Addt'l Rte.-Sec.: Crawford 64-2; Sebastian 540-1, 64-1	540	2	Miscellaneous	Programmed			-	< \$1 M	-	< \$1 M
012168	Okla. St. Line – Lamar (Sel. Secs.) (Cable Median Barrier) (S) Addt'l Rte.-Sec.: Johnson 40-21	40	11	Safety Improvements	Completed	Jan. 2013	Sep. 2013	10.47	\$1,562,527	27.77	\$4,144,352
012215	Alma – Bella Vista Bypass (Signing) (S) Addt'l Rte.-Sec.: Benton 49-29; Washington 49-28	49	27	Safety Improvements	Completed	Oct. 2018	Jun. 2019	20.47	\$2,847,697	71.75	\$9,981,545
012295	Districts 4 & 9 Pavement Friction Impvts. (Sel. Secs.) (S) Addt'l Rte.-Sec.: Various	540	19	Safety Improvements	Completed	Feb. 2018	May. 2019	1.02	\$535,524	9.71	\$5,095,739
012361*	Statewide UTBWC Impvts. (2020) (S) Addt'l Rte.-Sec.: Various	540	0	Safety Improvements	Under Construction	Nov. 2020	Late 2022	0.19	\$54,896	31.98	\$9,240,000
012372	Alma – Hwy. 164 (S) Addt'l Rte.-Sec.: Franklin 40-12; Johnson 40-21	40	11	Rehabilitation	Sub. Completed	Jun. 2020	Nov. 2021	7.54	\$11,282,651	29.57	\$44,247,742
012379	Specialized Bridge Deck Rehab. (2021) (S) Addt'l Rte.-Sec.: Various	64	2	Bridge Rehabilitation	Under Construction	Apr. 2021	Late 2022	0.04	\$425,826	1.80	\$19,162,121
012397*	I-40 Cable Median Barrier Impvts. (S) Addt'l Rte.-Sec.: Franklin 40-12; Johnson 40-21; Pope 40-22	40	11	Safety Improvements	Scheduled	Sep. 2022		5.49	\$1 - \$3 M	20.96	\$3 - \$5 M
012408*	Districts 4, 8 & 9 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various	64	2	Bridge Rehabilitation	Under Construction	Jun. 2022		-	\$187,055	-	\$8,575,000
012427*	Districts 4, 8 & 9 Centerline Rumble Stripe Impvts. (S) Addt'l Rte.-Sec.: Various			Safety Improvements	Under Construction	May. 2022	Mid 2025	7.08	\$45,113	312.35	\$1,990,253
040086*	Alma Weigh Station Reconstruction (S)	40	11	Roadside Appurtenances	Programmed			-	\$5 - \$10 M	-	\$5 - \$10 M
040128*	Lee Creek – Devil's Den	New		PE Only	Programmed			-	-	-	-
040178*	Okla. Line – I-40 (I-540) P.E. Addt'l Rte.-Sec.: Sebastian 540-1	540	2	PE Only	Programmed			-	-	-	-
040206	Lee Creek – East (S)	New		Reconstruction	Completed	Apr. 2015	Feb. 2017	3.56	\$4,541,668	3.56	\$4,541,668
040207	Devil's Den – West (S) Addt'l Rte.-Sec.: Washington 220-3	220	2	Reconstruction	Completed	Dec. 2015	Apr. 2018	1.91	\$4,663,589	3.87	\$9,449,260

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

CRAWFORD COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
040217*	I-40 & I-540 Landscaping (Ft. Smith/Van Buren) (S) Addt'l Rte.-Sec.: Sebastian 40-11, 540-1	540	2	Enhancement	Programmed			-	< \$1 M	-	< \$1 M
040296*	Lee Creek Trail (S)	New		Enhancement	Completed	May. 2008	Aug. 2013	-	\$127,092	-	\$127,092
040298*	Alma Weigh Station (Scale) (S)	40	11	Roadside Appurtenances	Programmed			-	< \$1 M	-	< \$1 M
040345*	Hwy. 59 – West (Rena Road) (Van Buren) (S)	CS		Major Widening Structure & Approaches	Completed	Oct. 2011	May. 2014	1.08	\$4,470,079	1.08	\$4,470,079
040373*	Hwy. 22 – I-40 (I-49) P.E.	New		PE Only	Completed		Jun. 2019	-	\$4,256,181	-	\$4,256,181
040456	Hwy. 162 Improvements (Alma) (S)	New		New Location	Completed	Oct. 2015	Jul. 2017	0.74	\$9,593,293	0.74	\$9,593,293
040464	Graphic Road – West (Wire Road) (Mulberry) (S)	CS		Reconstruction	Completed	Feb. 2014	Jul. 2015	0.94	\$1,098,239	0.94	\$1,098,239
040492*	I-40 – Fayetteville P.E. Addt'l Rte.-Sec.: Washington 49-28	49	27	PE Only	Programmed			-	-	-	-
040574*	Hwy. 59 RR Surf, (Van Buren) (S)	59	6	RR Crossing	Completed	Sep. 2011	May. 2013	-	\$75,066	-	\$75,066
040575*	Van Buren Intermodal Port Facility Access Impvts. (S)	CS		Study	Programmed			-	< \$1 M	-	< \$1 M
040622	Washington Co. Line – South Strs. & Apprs. (S)	59	5	Structure & Approaches	Under Construction	Jun. 2020	Jul. 2022	0.87	\$8,871,519	0.87	\$8,871,519
040623	Natural Dam – North Strs. & Apprs. (S)	59	5	Structure & Approaches	Completed	Aug. 2016	Apr. 2018	0.58	\$6,475,000	0.58	\$6,475,000
040631*	Mulberry SRTS I (2011)			Miscellaneous	Completed	Mar. 2014	Nov. 2014	-	\$101,310	-	\$101,310
040643	Chester – Hwy. 74 Slide Repair (S) Addt'l Rte.-Sec.: Washington 540-4	540	3	Base Stabilization	Completed	Sep. 2012	Apr. 2013	0.22	\$1,679,200	0.62	\$4,797,712
040652	N. Ham Town Rd. – East & West (Mulberry) (Overlay) (S)	64	2	Resurfacing	Completed	Jun. 2013	Aug. 2013	2.11	\$598,341	2.11	\$598,341
040669	Arkansas River – Flat Rock Creek (Overlay) (S)	64	2	Resurfacing	Completed	Apr. 2014	Aug. 2014	2.50	\$1,107,308	2.50	\$1,107,308
040678*	Orrick Rd. RR Signal (Alma) (S)			RR Crossing	Completed	Oct. 2014	Apr. 2017	-	\$165,911	-	\$165,911
040684	Hwy. 71 & Hwy. 282 Signal (Crawford Co.) (S) Addt'l Rte.-Sec.: Crawford 282-1	71	15	Safety Improvements	Completed	Apr. 2018	Mar. 2019	-	\$284,732	-	\$284,732
040686	Hwy. 64 – North (Alma) (S) Addt'l Rte.-Sec.: Crawford 162-1	71	15	Resurfacing	Completed	May. 2017	Nov. 2017	1.59	\$1,015,648	1.59	\$1,015,648
040694*	Alma Virtual Weigh Station Installation (S)	64	2	Roadside Appurtenances	Completed	Mar. 2016	Feb. 2017	0.06	\$904,515	0.06	\$904,515
040695*	Alma Weigh Station WIM Upgrade (S)	40	11	Roadside Appurtenances	Programmed			-	-	-	-
040696*	I-40/Ridge Rd. Impvt. Study (Dyer) (S)	40	11	Study	Programmed			-	-	-	-
040704*	Fayetteville Ave. Streetscape (Alma) (TAP-15) (S)			Enhancement	Completed	Dec. 2018	Dec. 2020	-	\$2,938,318	-	\$2,938,318
040705*	Hwy. 71 Sidewalk (Mountainburg) (TAP-15) (S)			Enhancement	Completed	Nov. 2017	Jul. 2018	-	\$179,610	-	\$179,610
040706*	N. Main St. & Hwy. 64 Sidewalks (Mulberry) (TAP-15) (S)			Enhancement	Completed	Jul. 2017	Sep. 2019	-	\$292,578	-	\$292,578

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

CRAWFORD COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
040707*	Rena Road Sidewalks (Van Buren) (TAP-15) (S)			Enhancement	Completed	Mar. 2017	Dec. 2019	-	\$254,598	-	\$254,598
040710*	Shibley Rd. RR Signals (E. of Van Buren) (S)	CR		RR Crossing	Programmed			-	< \$1 M	-	< \$1 M
040711*	N. 3rd St. RR Signals (Van Buren) (S)			RR Crossing	Completed	Sep. 2017	Feb. 2022	-	\$411,912	-	\$411,912
040712	Hwy. 59 Emergency Slope Failure Repair (Crawford Co.) (S)	59	5	Base Stabilization	Completed	Mar. 2016	Aug. 2016	0.11	\$886,025	0.11	\$886,025
040714	I-40/Hwy. 59 Interchange Impvts. (Van Buren) (S)	40	11	Safety Improvements	Scheduled	Jan. 2023		-	\$10 - \$15 M	-	\$10 - \$15 M
040718*	I-540 & Hwy. 22 Impvt. Study (Fort Smith & Van Buren) (S) Addt'l Rte.-Sec.: Sebastian 540-1/2	22	1	Study	Programmed			2.07	-	10.22	-
040721	Fayetteville Ave. – Hwy. 162 (Alma) (S)	64	2C	Enhancement Structure & Approaches	Scheduled	Apr. 2023		0.27	\$3 - \$5 M	0.27	\$3 - \$5 M
040728	Hwy. 64 – Hwy. 71 (S)	282	1	Resurfacing	Completed	May. 2017	Sep. 2017	10.06	\$1,674,097	10.06	\$1,674,097
040731	Hwy. 162 – Hwy. 64 (S)	64	2C	Resurfacing	Completed	Apr. 2017	Jul. 2017	1.08	\$372,908	1.08	\$372,908
040735*	Alma Sidewalks (TAP-16) (S)			Enhancement	Completed	Aug. 2020	Jun. 2021	2.18	\$774,811	2.18	\$774,811
040736*	Dyer Sidewalks (TAP-16) (S)			Enhancement	Completed	May. 2019	Dec. 2021	-	\$58,607	-	\$58,607
040737*	Van Buren Pointer Trail Sidewalks (TAP-16) (S)			Enhancement	Completed	Jan. 2019	Feb. 2020	1.00	\$191,250	1.00	\$191,250
040748*	Hwy. 22 – I-40 (Arkansas River) P.E. Addt'l Rte.-Sec.: Sebastian New	New		PE Only	Programmed			11.72	-	13.56	-
040750	Hwy. 59 Slide Repair (Washington & Crawford Cos.) (S) Addt'l Rte.-Sec.: Washington 59-4	59	5	Base Stabilization	Completed	Oct. 2017	Aug. 2019	0.03	\$111,058	1.17	\$4,331,265
040756*	Alma Little Frog Bayou Walking Trail (RTP-17) (S)	New		Enhancement	Programmed			-	< \$1 M	-	< \$1 M
040779	Elmo Creek Str. & Apprs. (S)	220	2	Structure & Approaches	Scheduled	Nov. 2022		0.24	\$1 - \$3 M	0.24	\$1 - \$3 M
040788	Hwy. 64 Strs. & Apprs. (Mulberry) (S)	64	2	Structure & Approaches	Scheduled	Feb. 2023		-	\$5 - \$10 M	-	\$5 - \$10 M
040805	Hwys. 220 & 265 Flood Repairs (S) Addt'l Rte.-Sec.: Washington 220-3, 265-1	220	2	Base Stabilization Miscellaneous	Sub. Completed	Jun. 2020	Nov. 2021	5.32	\$2,537,019	7.13	\$3,400,177
040807*	Van Buren Downtown Streetscape (TAP-19) (S)	59	5	Enhancement	Programmed			-	< \$1 M	-	< \$1 M
040810*	Lake Alma Trails Ph. 1 (Alma) (RTP-19) (S)			Enhancement	Under Construction	Oct. 2021		-	\$330,525	-	\$330,525
040819	Hwys. 64, 96 & 252 Strs. & Apprs. (S) Addt'l Rte.-Sec.: Sebastian 96-3, 252-4	64	2	Structure & Approaches	Under Construction	Jun. 2020	Late 2022	0.02	\$193,409	0.83	\$8,026,445
040821	Hwy. 71 Slide Repairs (Crawford Co.) (S)	71	15	Base Stabilization	Completed	Jun. 2020	Dec. 2020	0.58	\$3,409,942	0.58	\$3,409,942
040822*	District 4 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	220	1	Sealing	Completed		Jun. 2022	4.00	\$116,414	48.95	\$1,424,633

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

CRAWFORD COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
040824*	Mulberry Church Ave. Sidewalks (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
040825*	Van Buren Northridge Dr. Sidewalk Impvts. (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
040826	Hwy. 22 – I-40 (Sel. Secs.) (S) Addt'l Rte.-Sec.: Sebastian 540-1	540	2	Resurfacing	Scheduled	Feb. 2023		2.87	\$3 - \$5 M	7.39	\$10 - \$15 M
040827	Cedarville – Van Buren (Sel. Secs.) (S)	59	5	Resurfacing	Scheduled	Apr. 2023		12.45	\$3 - \$5 M	12.45	\$3 - \$5 M
040845	I-40 – Hwy. 282 Spur (F)	49	27	Reconstruction	Programmed			10.21	\$3 - \$5 M	10.21	\$3 - \$5 M
040853	Hwy. 162 Slide Repair (Crawford Co.) (S)	162	1	Base Stabilization	Completed	May. 2021	Jul. 2021	0.05	\$714,081	0.05	\$714,081
040872	Pointer Trl. – McKibben St. (Van Buren) (Widening) (S)	59	5	Major Widening	Scheduled	Nov. 2025		1.20	\$5 - \$10 M	1.20	\$5 - \$10 M
040884	I-40 – Hwy. 282 (S)	71	15	Resurfacing	Scheduled	2024		4.12	\$1 - \$3 M	4.12	\$1 - \$3 M
040885	Hwy. 59 Realignment (Crawford Co.) (S)	59	5	New Location	Programmed			0.21	\$1 - \$3 M	0.21	\$1 - \$3 M
040895*	I-49 & I-540 Cable Median Barrier Impvts. (S) Addt'l Rte.-Sec.: Crawford 540-2; Washington 49-28	49	27	Safety Improvements	Scheduled	Apr. 2023		12.88	\$1 - \$3 M	23.49	\$5 - \$10 M
040897	Hwy. 59 Slide Repair (Crawford Co.) (S)	59	5	Base Stabilization	Sub. Completed	Mar. 2022	Apr. 2022	-	\$847,773	-	\$847,773
040901	Hwy. 22 – Gun Club Rd. (S) Addt'l Rte.-Sec.: Sebastian New	New		New Location	Scheduled	Sep. 2024		1.31	\$100 - \$125 M	3.10	\$250 - \$300 M
040902	Gun Club Rd. – Clear Creek Rd. (S)	New		New Location	Programmed			6.31	\$100 - \$125 M	6.31	\$100 - \$125 M
040903	Clear Creek Rd. – I-40 (S)	New		New Location	Programmed			4.40	\$75 - \$100 M	4.40	\$75 - \$100 M
040904	I-40/I-49 Interchange Impvts. (S) Addt'l Rte.-Sec.: Crawford 49-0	40	11	Safety Improvements	Scheduled	2025		-	\$200 - \$250 M	-	\$200 - \$250 M
A40003	I-40 – Mt. Vista Blvd. (Van Buren) (S)	59	5	Resurfacing	Completed	May. 2020	Aug. 2020	1.13	\$823,008	1.13	\$823,008
A40004	Hwy. 64 – Hwy. 22 (S) Addt'l Rte.-Sec.: Sebastian 59-7	59	6	Resurfacing	Sub. Completed	Apr. 2020	Dec. 2020	6.89	\$3,752,259	8.63	\$4,693,027
A40007*	District 4 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	60	8	Resurfacing	Completed		Jun. 2022	1.31	\$25,785	64.70	\$1,273,514
A40009	Frog Bayou Str. & Apprs. (S)	282	2	Structure & Approaches	Scheduled	Nov. 2023		-	< \$1 M	-	< \$1 M
A40011	I-540 – Hwy. 162 (S)	64	2	Resurfacing	Under Construction	Apr. 2022	Jul. 2022	5.80	\$5,244,444	5.80	\$5,244,444
A40016*	District 4 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	220	1	Resurfacing	Programmed			3.97	< \$1 M	38.66	\$1 - \$3 M
BB0401	Oklahoma State Line – East (I-40 & I-540) (Sel. Secs.) (S) Addt'l Rte.-Sec.: Crawford 540-2, CS, 60-8; Sebastian 540-1	40	11	Bridge Rehabilitation Resurfacing	Completed	Oct. 2018	Aug. 2020	17.00	\$41,523,808	20.83	\$53,245,517

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

CRAWFORD COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
BB0403	Dyer – Cravens Creek (S) Addt'l Rte.-Sec.: Franklin 40-12	40	11	Resurfacing	Completed	Feb. 2013	Aug. 2013	7.43	\$4,926,363	13.86	\$9,122,895
BB0407	Hwy. 22 – I-40 (F) Addt'l Rte.-Sec.: Sebastian 540-1	540	2	Reconstruction	Completed	Nov. 2012	May. 2014	2.87	\$28,411,451	7.46	\$78,914,029
BB0409	I-49 Pavement Rehabilitation (Sel. Secs.) (S) Addt'l Rte.-Sec.: Washington 49-28	49	27	Rehabilitation	Completed	Oct. 2015	Jun. 2018	7.70	\$5,985,638	28.39	\$22,169,030
C17002*	Van Buren 28th St. Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Apr. 2015	Aug. 2015	0.65	\$252,082	0.65	\$252,082
C17003*	Cedarville Mill Pond Rd. (Reconstruction) (S)	CS		Reconstruction	Completed	Jul. 2015	Apr. 2016	0.35	\$314,588	0.35	\$314,588
C17004*	Dyer Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Apr. 2015	Sep. 2015	1.04	\$279,502	1.04	\$279,502
C17005*	Chester Overlay & Surfacing (Sel. Secs.) (S)	CS		Resurfacing	Completed	Apr. 2015	Sep. 2015	0.90	\$189,809	0.90	\$189,809
C17006*	Alma & Kibler Overly (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jul. 2017	Nov. 2017	3.47	\$522,640	3.47	\$522,640
C17008*	Dyer, Mulberry & Rudy Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Apr. 2018	Sep. 2018	4.07	\$730,346	4.07	\$730,346
C17009*	Alma Rudy Rd. Overlay (S)	CS		Resurfacing	Completed	Apr. 2021	Nov. 2021	1.71	\$469,359	1.71	\$469,359
C76034*	Mountainburg & Winslow Overlay (Sel Secs) (S) Addt'l Rte.-Sec.: Washington CS	CS		Resurfacing	Completed	Jun. 2016	Sep. 2016	1.92	\$237,376	3.89	\$484,441
SA1766*	Crawford County Overlay No 4 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2012	Oct. 2012	5.10	\$646,209	5.10	\$646,209
SA1767*	Zion Rd. - North Overlay (S)	CR		Resurfacing	Completed	Jun. 2013	Jul. 2013	1.70	\$289,878	1.70	\$289,878
SA1768*	Crawford County Overlay No. 5 (Sel. Secs.)(s)	CR		Resurfacing	Completed	Sep. 2014	Nov. 2014	-	\$274,957	-	\$274,957
SA1769*	Co. Rd. 63 Overlay (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2015	Oct. 2015	2.30	\$370,418	2.30	\$370,418
SA1770*	Hwy 162 - North (Sunnyside Rd.) (Overlay) (S)	CR		Resurfacing	Completed	Sep. 2016	Nov. 2016	1.95	\$329,677	1.95	\$329,677
SA1771*	Hwy. 60 - North (Overlay) (S)	CR		Resurfacing	Completed	May. 2018	Aug. 2018	2.90	\$570,297	2.90	\$570,297
SA1772*	Hwy. 59 - Pine Hollow Rd. (Overlay) (S)	CR		Resurfacing	Sub. Completed	Jan. 2022	Apr. 2022	1.62	\$413,827	1.62	\$413,827
Totals For All Projects In Crawford County								208.04	\$573,426,002		

* Job not shown on county map.
