



Status of Improvements

- Programmed
- Scheduled
- Under Construction
- Completed
- Bridge
- ◆ Interchange
- ⊕ Intersection Improvement
- ⊙ Slide Repair
- Roadway
- New Location

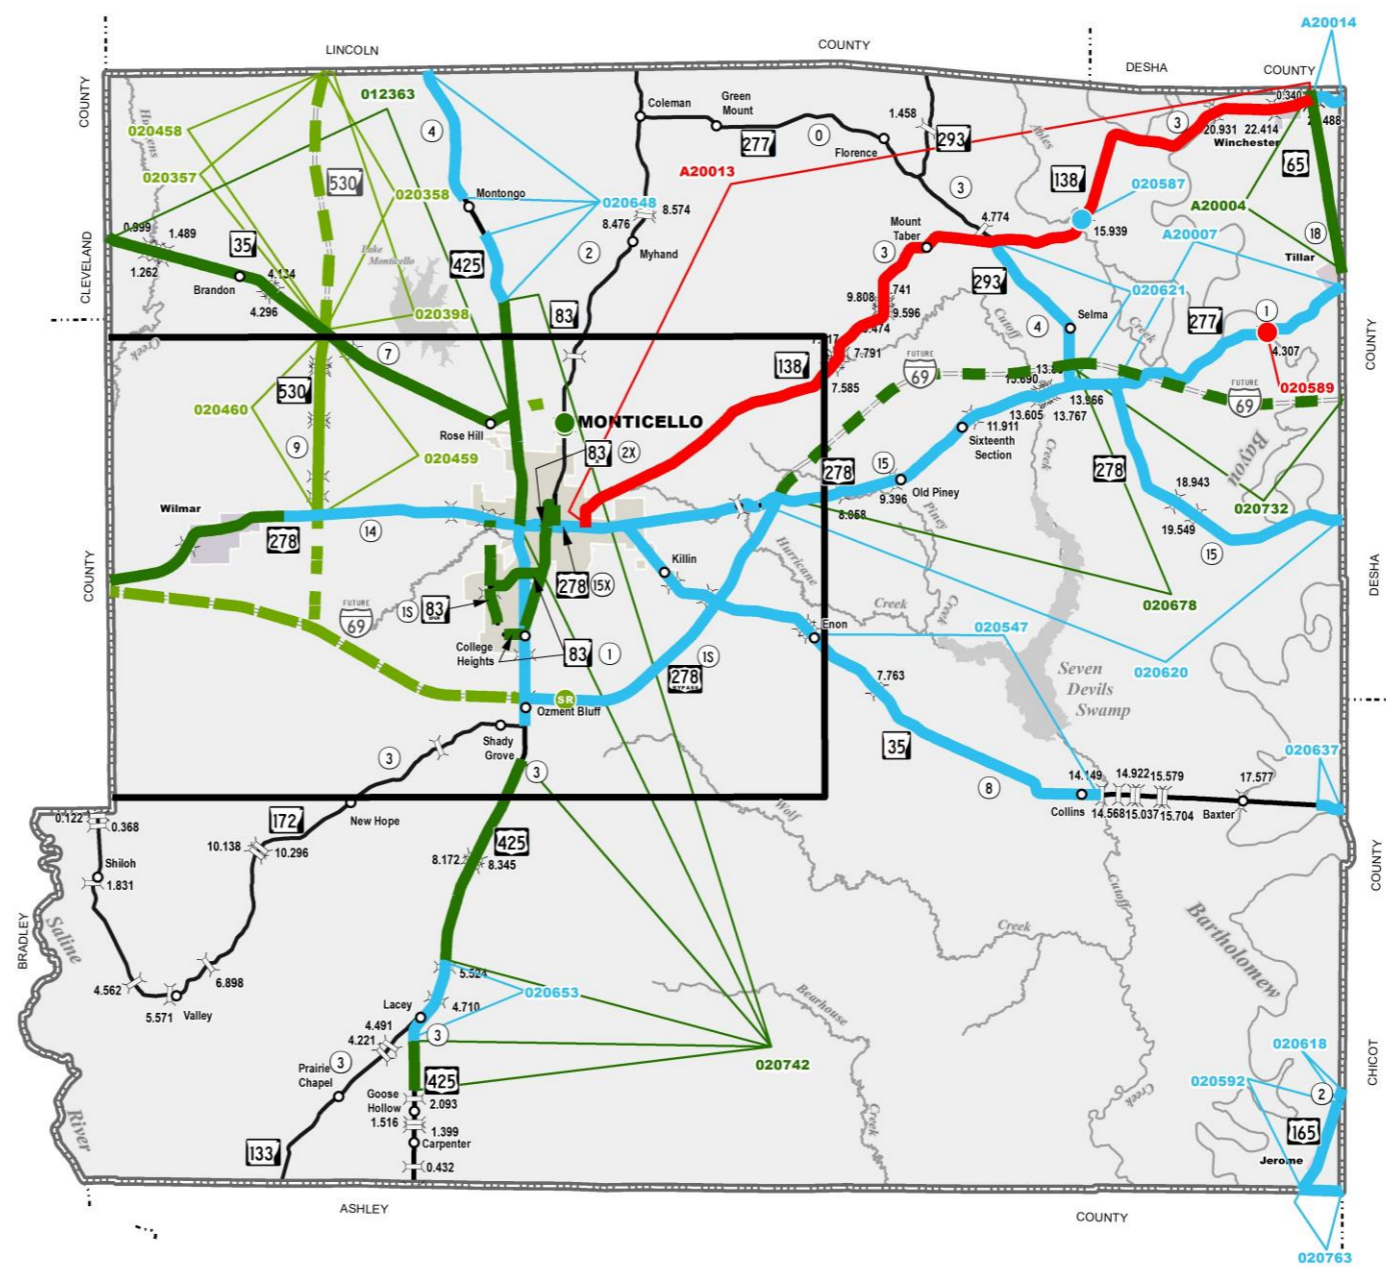

AR DOT
ARIZONA DEPARTMENT OF TRANSPORTATION

Drew County
District 2
Job Status Map

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
012062*	I-69 Connector Extension Study (F) Addt'l Rte.-Sec.: Ashley 530-10; Bradley 530-11; Union 530-12	530	9	Study	Completed	Aug. 2006	May. 2014	-	\$573,120	-	\$1,135,620
012361*	Statewide UTBWC Impvts. (2020) (S) Addt'l Rte.-Sec.: Various	278	15	Safety Improvements	Under Construction	Nov. 2020	Late 2022	0.41	\$118,461	31.98	\$9,240,000
012363	Big Creek – Hwy. 425 (Sel. Secs.) (S) Addt'l Rte.-Sec.: Cleveland 35-5/6	35	7	Resurfacing	Scheduled	2023		11.13	\$3 - \$5 M	17.58	\$5 - \$10 M
012375*	Districts 1, 2 & 6 Bridge Preservation (2021) (S) Addt'l Rte.-Sec.: Lincoln 114-2; Phillips 20-1, 44-3; Saline 35-1	83	1	Bridge Rehabilitation	Under Construction	May. 2021	Jul. 2022	0.04	\$831,771	0.20	\$4,158,856
012407*	Districts 2, 3 & 7 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various	138	3	Bridge Rehabilitation	Under Construction	Apr. 2022	Mid 2023	-	\$62,989	-	\$5,195,000
012425*	Districts 2 & 6 Centerline Rumble Stripe Impvts. (S)			Safety Improvements	Under Construction	Apr. 2022	Early 2023	51.82	\$343,973	443.88	\$2,946,406
020311	Hwy. 425 – Hwy. 83 Connection (Monticello) (S)	New		New Location	Programmed			1.20	\$1 - \$3 M	1.20	\$1 - \$3 M
020357	Hwys. 11/425 Connector – Hwy. 35 (Gr. & Strs.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Grading & Structures	Programmed			6.32	\$15 - \$20 M	10.45	\$20 - \$30 M
020358	Hwys. 11/425 Connector – Hwy. 35 (Bs. & Surf.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Base & Surfacing	Programmed			6.58	\$20 - \$30 M	11.07	\$30 - \$40 M
020365*	Hwys. 11/425 Connector – Hwy. 278 P.E. Addt'l Rte.-Sec.: Lincoln New	New		PE Only	Completed			-	\$0	-	\$6,734,428
020398	Hwys. 11/425 Connector – Hwy. 35 (Add'l. Lanes) (Gr. & Strs.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Grading & Structures	Programmed			6.50	\$30 - \$40 M	10.50	\$50 - \$75 M
020458	Hwys. 11/425 Connector – Hwy. 35 (Add'l. Lanes) (Bs. & Surf.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Base & Surfacing	Programmed			6.50	\$20 - \$30 M	10.50	\$30 - \$40 M
020459	Hwy. 35 – Hwy. 278 (Add'l. Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			4.50	\$20 - \$30 M	4.50	\$20 - \$30 M
020460	Hwy. 35 – Hwy. 278 (Add'l. Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			4.50	\$10 - \$15 M	4.50	\$10 - \$15 M
020462*	Monticello Bypass P.E.	New		PE Only	Programmed			-	\$50 - \$75 M	-	\$50 - \$75 M
020470	Hwy. 278 West – Hwy. 425 (Gr. & MDS) (Monticello Bypass) (S)	New		Grading & Structures	Programmed			13.39	\$20 - \$30 M	13.39	\$20 - \$30 M
020471	Hwy. 425 – Hwy. 278 East (Gr. & Strs.) (Monticello Bypass) (F)	New		Grading & Structures	Completed	Sep. 2011	Oct. 2017	8.53	\$13,159,489	8.53	\$13,159,489
020475	Hwy. 83 Spur – Hwy. 278 Connector (Monticello) (F)	New		New Location	Scheduled	Nov. 2022		1.68	\$20 - \$30 M	1.68	\$20 - \$30 M
020480*	Southeast Arkansas Intermodal Facility (Ph. II) (Wilmar) (S)			Roadside Appurtenances	Programmed			-	< \$1 M	-	< \$1 M
020482	Hwy. 278 West – Hwy. 425 (Add'l Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			11.30	-	11.30	-
020483	Hwy. 278 West – Hwy. 425 (Add'l Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			11.30	-	11.30	-

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
020484	Hwy. 425 – Hwy. 278 East (Bs. & Surf.) (Monticello Bypass) (S)	New		Base & Surfacing	Completed	Aug. 2017	Oct. 2018	8.63	\$16,197,356	8.63	\$16,197,356
020485	Hwy. 425 – Hwy. 278 East (Add'l Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			8.60	-	8.60	-
020486	Hwy. 425 – Hwy. 278 East (Add'l Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			8.60	-	8.60	-
020518*	Southeast Arkansas Intermodal Facility (Ph. III) (Wilmar) (S)			Roadside Appurtenances	Under Construction	Aug. 2011		-	\$622,151	-	\$622,151
020519*	Southeast Arkansas Intermodal Facility (Ph. IV) (Wilmar) (S)			Roadside Appurtenances	Under Construction	Jul. 2013		-	\$560,411	-	\$560,411
020532*	Monticello City Square Sidewalks (ATEP-11) (S)			Enhancement	Completed	Mar. 2013	Sep. 2013	-	\$134,200	-	\$134,200
020547	Sandy Creek – Cutoff Creek (Overlay) (S)	35	8	Resurfacing	Completed	May. 2012	Aug. 2012	8.59	\$1,807,499	8.59	\$1,807,499
020552*	Hwy. 35 R.R. Surfacing (Monticello) (S)	35	0	RR Crossing	Completed	Mar. 2013	Apr. 2014	-	\$80,674	-	\$80,674
020557	Hwy. 278 – Sandy Creek (Overlay) (S)	35	8	Resurfacing	Completed	Jun. 2013	Sep. 2013	5.65	\$1,304,110	5.65	\$1,304,110
020560*	Monticello School District SRTS I (2012)			Miscellaneous	Programmed			-	-	-	-
020564	Hwy. 425 (Monticello) (Sel. Sec.) (Overlay) (S) Addt'l Rte.-Sec.: Drew 425-4	425	3	Resurfacing	Completed	Apr. 2014	Aug. 2014	4.63	\$1,521,383	4.63	\$1,521,383
020587	Ables Creek Str. & Apprs. (S)	138	3	Structure & Approaches	Completed	Dec. 2018	Oct. 2020	0.34	\$3,204,170	0.34	\$3,204,170
020589	Bayou Bartholomew Str. & Apprs. (S)	277	1	Structure & Approaches	Under Construction	Jun. 2020	Late 2022	0.46	\$4,604,247	0.46	\$4,604,247
020592	Drew Co. Line – North & South (Mill & Inlay) (S) Addt'l Rte.-Sec.: Ashley 165-1	165	2	Resurfacing	Completed	Jun. 2016	Oct. 2016	2.40	\$467,111	9.34	\$1,817,843
020611	Hwy. 278 West – Hwy. 425 (Major Strs. & Surf.) (Monticello Bypass) (S)	New		Base & Surfacing	Programmed			13.39	\$15 - \$20 M	13.39	\$15 - \$20 M
020618	South of Drew Co. Line – Hwy. 35 (Sel. Secs.) (S) Addt'l Rte.-Sec.: Chicot 165-3	165	2	Bridge Rehabilitation Resurfacing	Completed	Feb. 2018	Nov. 2018	0.13	\$30,627	5.76	\$1,357,033
020620	Monticello – McGehee (Sel. Secs.) (S) Addt'l Rte.-Sec.: Desha 278-16	278	15	Resurfacing	Completed	Jan. 2018	Jul. 2018	20.22	\$3,788,797	24.91	\$4,667,602
020621	Hwy. 138 – Hwy. 278 (S)	293	4	Resurfacing	Completed	May. 2018	Oct. 2018	4.27	\$1,355,760	4.27	\$1,355,760
020635	Hwy. 172 – Old Warren Rd. (Monticello) (S)	425	3	Resurfacing	Completed	Jan. 2017	Jul. 2017	4.03	\$2,208,708	4.03	\$2,208,708
020637	West of Drew Co. Line – Hwy. 65 (S) Addt'l Rte.-Sec.: Chicot 35-9	35	8	Resurfacing	Completed	Apr. 2017	Oct. 2017	0.71	\$205,554	5.33	\$1,543,104
020648	Monticello – Star City (Sel. Secs.) (S) Addt'l Rte.-Sec.: Lincoln 425-5	425	4	Resurfacing	Completed	Feb. 2020	Sep. 2020	5.18	\$1,811,638	9.38	\$3,294,851
020653	Co. Rd. 28 – South (S)	425	3	Resurfacing	Completed	Feb. 2020	Oct. 2020	2.15	\$714,297	2.15	\$714,297
020669*	Lake Monticello Trail (TAP-16) (S)			Miscellaneous	Programmed			-	< \$1 M	-	< \$1 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
020678	Hwy. 278 – Hwy. 293 (S)	New		New Location	Scheduled	Aug. 2022		8.25	\$50 - \$75 M	8.25	\$50 - \$75 M
020719*	Monticello Hwys. 278 & 425 Sidewalks (TAP-19) (S) Addt'l Rte.-Sec.: Drew 425-3/4	278	14	Enhancement	Programmed			-	< \$1 M	-	< \$1 M
020722	Hwy. 83 Resurfacing (Sel. Secs.) (Monticello) (S) Addt'l Rte.-Sec.: Drew 83-1S/2/2X, CS	83	1	Resurfacing	Scheduled	May. 2023		6.43	\$1 - \$3 M	6.43	\$1 - \$3 M
020726*	Hwy. 138 RR Signals (Winchester) (S)	138	3	Safety Improvements	Under Construction	May. 2021		-	\$350,000	-	\$350,000
020727*	District 2 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	144	1	Sealing	Completed		Jun. 2022	11.90	\$152,694	81.83	\$1,050,000
020732	Hwy. 293 – Hwy. 65 (S) Addt'l Rte.-Sec.: Desha New	New		New Location	Scheduled	May. 2025		6.74	\$40 - \$50 M	8.56	\$50 - \$75 M
020741	Bradley Co. Line – Wilmar (S)	278	14	Resurfacing	Scheduled	2024		4.80	\$3 - \$5 M	4.80	\$3 - \$5 M
020742	Ashley Co. Line – Monticello (Sel. Secs.) (S) Addt'l Rte.-Sec.: Drew 425-4	425	3	Resurfacing	Scheduled	2024		11.99	\$5 - \$10 M	11.99	\$5 - \$10 M
020763	Jerome – McMillan Corner (S) Addt'l Rte.-Sec.: Chicot 144-2	144	1	Resurfacing	Completed	May. 2021	Oct. 2021	0.99	\$411,146	9.27	\$3,849,823
020765*	Monticello County Library Sidewalks (TAP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
020767*	Lake Monticello Trail Ph. 1 (Monticello) (RTP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
020775	Hwy. 83 Strs. & Apprs. (S)	83	2	Structure & Approaches	Scheduled	Nov. 2023		0.25	\$1 - \$3 M	0.25	\$1 - \$3 M
020791	Hwys. 82, 270 & 278 Slide Repairs (S) Addt'l Rte.-Sec.: Ashley 82-9; Jefferson 270-11	278	15	Base Stabilization	Programmed			-	< \$1 M	-	< \$1 M
A20002	Wilmar – Monticello (S) Addt'l Rte.-Sec.: Drew 278-15/15X	278	14	Resurfacing	Completed	Apr. 2020	Oct. 2020	9.32	\$4,883,547	9.32	\$4,883,547
A20004	Winchester – Chicot Co. Line (Sel. Secs.) (S) Addt'l Rte.-Sec.: Desha 65-18/19	65	19	Resurfacing	Scheduled	Jun. 2022		6.24	\$1 - \$3 M	12.97	\$5 - \$10 M
A20007	Hwy. 278 – Hwy. 65 (S) Addt'l Rte.-Sec.: Desha 277-1	277	1	Resurfacing	Completed	Feb. 2021	Sep. 2021	6.09	\$1,658,361	6.22	\$1,693,761
A20010*	District 2 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	35	8	Resurfacing	Programmed			20.26	< \$1 M	75.48	< \$1 M
A20013	Monticello – Hwy. 65 (S)	138	3	Resurfacing	Under Construction	Jun. 2022		23.20	\$12,890,028	23.20	\$12,890,028
A20014	Hwy. 65 – Hwy. 1 (S) Addt'l Rte.-Sec.: Desha 138-4	138	3	Resurfacing	Sub. Completed	Jan. 2022	Jun. 2022	0.82	\$384,173	13.60	\$6,371,659

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
A20015*	District 2 Resurfacing Program (2022) (S) Addt'l Rte.-Sec.: Various	293	3	Resurfacing	Programmed			5.18	< \$1 M	47.54	\$1 - \$3 M
A20017*	District 2 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	172	3	Resurfacing	Programmed			12.18	< \$1 M	71.70	\$1 - \$3 M
C22001*	Wilamr Street Improvements (Sel. Secs.) (S)	CS		Resurfacing	Completed	Apr. 2014	Jul. 2014	1.53	\$255,339	1.53	\$255,339
C22002*	Wilmar Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jun. 2018	Aug. 2018	2.14	\$237,401	2.14	\$237,401
C22003*	Winchester Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jan. 2020	May. 2020	0.81	\$199,312	0.81	\$199,312
C22004*	Monticello Overlay (S)	CS		Resurfacing	Completed	May. 2020	Nov. 2020	1.36	\$264,851	1.36	\$264,851
C76006*	Monticello & Star City Overlay (Sel Secs) (S) Addt'l Rte.-Sec.: Lincoln CS	CS		Resurfacing	Completed	Jan. 2014	Mar. 2014	1.45	\$201,768	3.25	\$448,372
C76044*	Arkansas City, Dermott & Tillar Overlay (S) Addt'l Rte.-Sec.: Chicot CS; Desha CS	CS		Resurfacing	Completed	Feb. 2019	May. 2019	1.16	\$178,708	4.54	\$700,966
R20089*	Pine Bluff – Mississippi Line P.E. Addt'l Rte.-Sec.: Various	65	18	PE Only	Programmed			-	-	-	-
R20107*	La. Line – Pine Bluff P.E. Addt'l Rte.-Sec.: Various	425	3	PE Only	Programmed			-	-	-	-
SA2245*	Drew County Overlay (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2014	Oct. 2014	8.36	\$1,126,760	8.36	\$1,126,760
SA2246*	Drew County Overlay No. 2 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Aug. 2016	Oct. 2016	3.88	\$553,191	3.88	\$553,191
SA2247*	Co. Rd. 92 - Co. Rd. 99 (Overlay) (S)	CR		Resurfacing	Completed	Jul. 2018	Dec. 2018	3.45	\$439,958	3.45	\$439,958
SA2248*	Co. Rd. 47 - Hwy. 35 (Overlay) (S)	CR		Resurfacing	Under Construction	May. 2022	Late 2022	2.50	\$483,592	2.50	\$483,592
Totals For All Projects In Drew County								264.66	\$223,559,573		

* Job not shown on county map.
