


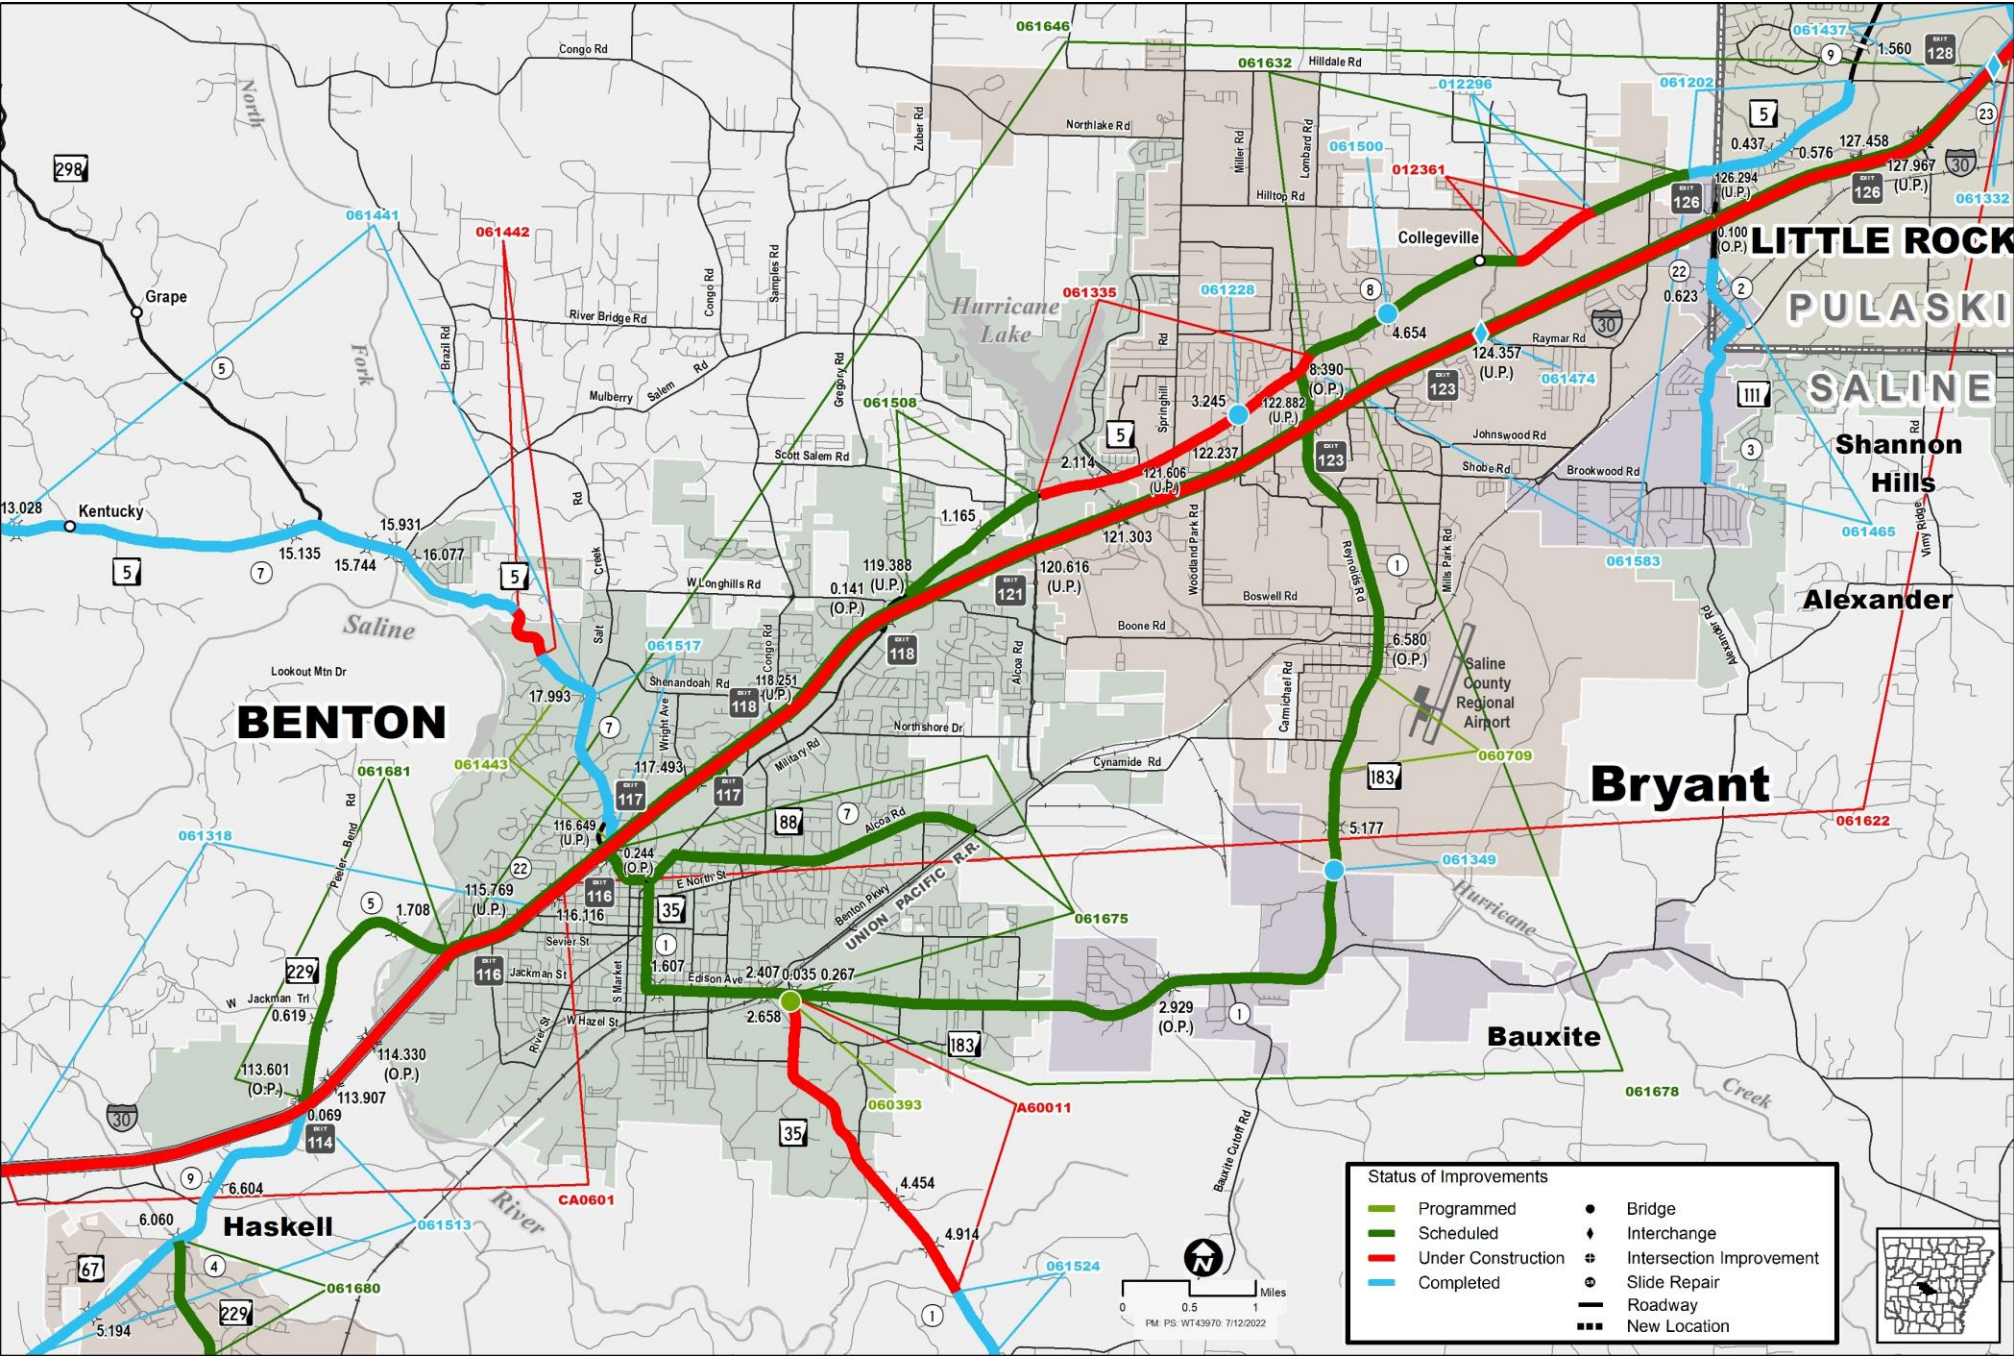

Benton/Bryant

District 6

Job Status Map

SUMMARY OF CONSTRUCTION PROJECTS

SALINE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
012149	Caddo Valley – Hwy. 70 (Sel. Secs.) (Cable Median Barrier) (F) Addt'l Rte.-Sec.: Clark 30-14; Hot Spring 30-21	30	22	Safety Improvements	Completed	May. 2012	Mar. 2013	1.32	\$270,406	17.27	\$3,862,951
012296	Districts 2, 6, 7 & 8 Pavement Friction Impvts. (Sel. Secs.) (S) Addt'l Rte.-Sec.: Various	5	8	Safety Improvements	Completed	Jan. 2018	Oct. 2018	0.85	\$361,199	6.10	\$2,648,885
012335*	Foot Trail Shelter Modifications (RTP-18) (S)			Enhancement	Completed	Oct. 2019	Mar. 2021	-	\$5,250	-	\$26,250
012361*	Statewide UTBWC Impvts. (2020) (S) Addt'l Rte.-Sec.: Various			Safety Improvements	Under Construction	Nov. 2020	Late 2022	1.86	\$537,411	31.98	\$9,240,000
012375*	Districts 1, 2 & 6 Bridge Preservation (2021) (S) Addt'l Rte.-Sec.: Drew 83-1; Lincoln 114-2; Phillips 20-1, 44-3	35	1	Bridge Rehabilitation	Under Construction	May. 2021	Jul. 2022	0.02	\$415,885	0.20	\$4,158,856
012406*	Districts 1, 5, 6 & 10 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various	35	1	Bridge Rehabilitation	Under Construction	May. 2022	Mid 2023	-	\$130,270	-	\$7,187,312
012425*	Districts 2 & 6 Centerline Rumble Stripe Impvts. (S)			Safety Improvements	Under Construction	Apr. 2022	Early 2023	2.01	\$13,342	443.88	\$2,946,406
060393	Depot Creek Br. & Apprs.	35	1	Structure & Approaches	Programmed			-	< \$1 M	-	< \$1 M
060709	Hwy. 183 Widening (S. of Bryant) (S)	183	1	Major Widening	Programmed			0.78	\$3 - \$5 M	0.78	\$3 - \$5 M
060783*	LTPP – SPS-2, Pavement Performance Study on Job 060616	30	22	Study	Programmed			-	< \$1 M	-	< \$1 M
061100*	Hwys. 35/88 Inters. Resurf. & Impvts. (Benton) (S)	35	1	Right of Way	Programmed			0.30	< \$1 M	0.30	< \$1 M
061202	Saline Co. Line – Otter Creek Rd. (Little Rock) (S) Addt'l Rte.-Sec.: Pulaski 5-9	5	8	Major Widening	Completed	Jun. 2011	Sep. 2014	0.22	\$2,190,765	1.49	\$14,837,447
061228	Hwy. 5 Drainage Structure (Bryant) (S)	5	8	Structure & Approaches	Completed	Sep. 2011	Aug. 2012	0.03	\$534,299	0.03	\$534,299
061232*	Benton South St. Streetscaping (S)			Enhancement	Completed	Apr. 2012	Jan. 2013	-	\$363,102	-	\$363,102
061257*	Congo Rd. – I-30 (Military Rd.) (Benton) (F)	CS		Major Widening	Completed	Feb. 2011	Sep. 2015	1.43	\$18,536,137	1.43	\$18,536,137
061262*	Benton – Pulaski Co. Line (Widening) P.E.	5	8	PE Only	Programmed			-	-	-	-
061297*	I-30 – Sidell Rd. (Alcoa Rd.) (Saline Co.) (S)	CS		Major Widening	Completed	Jul. 2016	Apr. 2019	1.87	\$14,609,107	1.87	\$14,609,107
061318	Hwy. 70 – Sevier St. (Benton) (Resurfacing) (F)	30	22	Resurfacing	Completed	May. 2012	Apr. 2013	5.55	\$6,582,508	5.55	\$6,582,508
061335	Alcoa Rd. – Hwy. 183 (S)	5	8	Major Widening Structure & Approaches	Under Construction	Sep. 2018	Late 2022	2.31	\$17,394,676	2.31	\$17,394,676
061341*	Upper Saline River Mitigation Bank (S)			Study	Programmed			-	-	-	-
061349	Bauxite & Northern RR Spur Str. & Apprs. (S)	183	1	Structure & Approaches	Completed	Jan. 2016	Oct. 2016	0.53	\$3,433,679	0.53	\$3,433,679
061362*	Haskell SRTS E (2011)			Miscellaneous	Completed	Apr. 2012	Jul. 2014	-	\$4,443	-	\$4,443
061365*	Haskell SRTS I (2011)			Miscellaneous	Completed	Jan. 2013	Jun. 2013	-	\$25,439	-	\$25,439
061387*	Benton South St. Streetscaping (Ph. II) (Benton) (S)	CS		Enhancement	Completed	Dec. 2013	Mar. 2015	-	\$213,253	-	\$213,253

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

SALINE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
061403*	Bishop Park Trail (Bryant) (S)			Enhancement	Completed		Jun. 2016	-	\$13,750	-	\$13,750
061404*	Shannon Hills City Park Trail (S)			Enhancement	Completed	Oct. 2014	Apr. 2016	-	\$66,640	-	\$66,640
061418*	Shannon Hills SRTS I (2012)			Miscellaneous	Under Construction	Feb. 2020		-	\$177,573	-	\$177,573
061419*	Haskell SRTS I (2012)			Miscellaneous	Completed	Oct. 2014	May. 2015	-	\$69,600	-	\$69,600
061441	Hwy. 128 – Benton (Safety Impvts.) (S) Addt'l Rte.-Sec.: Garland 5-6	5	7	Safety Improvements	Completed	Feb. 2016	Sep. 2017	17.75	\$6,696,574	20.93	\$7,896,298
061442	Garland Co. Line – Benton (Safety Impvts.) (S)	5	7	Safety Improvements	Under Construction	Nov. 2020	Jul. 2022	3.20	\$8,230,124	3.20	\$8,230,124
061443	Salt Creek Rd. – I-30 (Widening) (S)	5	7	Major Widening Safety Improvements	Programmed			1.40	\$10 - \$15 M	1.40	\$10 - \$15 M
061444*	Benton – South Terminal Interchange (I-30 Corridor Study) (S) Addt'l Rte.-Sec.: Pulaski 30-22	30	23	Study	Completed	Jan. 2020	Mar. 2020	-	\$363	21.57	\$781,615
061465	I-30 – South (Overlay) (S) Addt'l Rte.-Sec.: Pulaski 111-2	111	3	Resurfacing	Completed	Mar. 2016	Aug. 2016	1.05	\$172,105	1.89	\$309,789
061470*	Hwy. 183 Jump Start Impvts. (Bryant) (S)	183	1	Miscellaneous	Under Construction	Nov. 2017		0.44	\$1,625,024	0.44	\$1,625,024
061474	Bryant Pkwy. Interchange (Bryant) (S)	30	22	Interchange Improvements	Completed	Jan. 2017	Jun. 2017	1.46	\$6,901,236	1.46	\$6,901,236
061478*	Riverside Park Trail (Benton) (RTP-15) (S)			Enhancement	Completed	Jan. 2017	Dec. 2017	-	\$241,485	-	\$241,485
061482*	Joan Dr. Sidewalks (Shannon Hills) (SRTS-15) (S)			Enhancement	Completed	Feb. 2020	Oct. 2020	-	\$339,874	-	\$339,874
061497*	Shannon Hills Recreational Trails (Ph. 1) (TAP-15) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061498*	Old River Bridge Rehab. (Saline Co.) (TAP-15) (S)			Enhancement	Completed	Dec. 2017	Sep. 2018	-	\$472,730	-	\$472,730
061500	Creek at L.M. 4.65 Str. & Apprs. (S)	5	8	Structure & Approaches	Completed	May. 2018	Sep. 2018	0.03	\$628,662	0.03	\$628,662
061502*	Jackman St. & River St. Sidewalks (Benton) (S)			Enhancement	Programmed			-	-	-	-
061508	I-30 – Alcoa Rd. (Benton) (S)	5	8	Major Widening	Scheduled	Apr. 2023		1.20	\$10 - \$15 M	1.20	\$10 - \$15 M
061513	Hot Spring Co. Line – I-30 (S) Addt'l Rte.-Sec.: Saline 229-5	67	9	Resurfacing	Completed	Aug. 2017	Jan. 2018	7.66	\$1,768,138	7.66	\$1,768,138
061517	Salt Creek Rd. – I-30 (Benton) (S)	5	7	Resurfacing	Completed	Apr. 2019	Aug. 2019	1.18	\$442,088	1.18	\$442,088
061524	Holly Creek – Hwy. 190 (S)	35	1	Resurfacing	Completed	Jan. 2019	Oct. 2019	2.08	\$363,358	2.08	\$363,358
061533*	Saline County Crossing at Angel Court Trail (RTP-16) (S)			Enhancement	Completed	Jun. 2018	Dec. 2018	-	\$179,988	-	\$179,988
061542*	Benton Riverside Trail Ph. 2 (TAP-16) (S)			Enhancement	Completed	Nov. 2017	Jan. 2021	-	\$205,410	-	\$205,410
061543*	Bryant Mills Park Trail (TAP-16) (S)			Enhancement	Completed	Mar. 2020	Feb. 2021	-	\$45,945	-	\$45,945
061544*	Shannon Hills Sidewalks (TAP-16) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061561	Hwy. 5 – Perry Co. Line (Safety Impvts.) (Sel. Secs.) (S)	9	5	Safety Improvements	Completed	Jul. 2018	Jul. 2019	16.80	\$8,834,871	16.80	\$8,834,871

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
SALINE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
061562*	Southwest Trail Design Addt'l Rte.-Sec.: Garland New; Pulaski New	New		Enhancement	Programmed			-	< \$1 M	-	\$1 - \$3 M
061563*	Congo Rd./Longhills Rd. Inters. Impvts. (Benton) (S)	CS		Safety Improvements	Completed	Aug. 2019	Apr. 2020	-	\$509,893	-	\$509,893
061571*	Benton Southwest Trail Loop Connector (RTP-17) (S)	New		Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061572*	Vimy Ridge Rd./County Line Rd. Inters. Impvts. (Shannon Hills) (S)			Safety Improvements	Under Construction	Jan. 2020		-	\$151,718	-	\$303,435
061573*	Springlake Roundabout (Saline Co.) (S)	CR		Safety Improvements	Under Construction	Oct. 2021		-	\$779,727	-	\$779,727
061581*	Davis Elementary Trail (Shannon Hills) (S)	New		Enhancement	Under Construction	May. 2021		-	\$150,567	-	\$150,567
061583	Hwy. 183 – Pulaski Co. Line (Bryant) (S)	5	8	Resurfacing	Completed	May. 2020	Nov. 2020	3.33	\$761,073	3.33	\$761,073
061598	I-530/Hwy. 167 Intchn. Ramps (S)	167	12	Resurfacing	Completed	Apr. 2020	Jun. 2020	1.33	\$262,922	1.33	\$262,922
061604*	Saline County Old River Bridge Ph. 2			Enhancement	Under Construction	Jul. 2021		-	\$3,111,764	-	\$3,111,764
061607*	Bryant Pkwy./Hilldale Rd./Hilltop Rd. Roundabout (S)	CS		Safety Improvements	Completed	Mar. 2021	Dec. 2021	-	\$932,466	-	\$932,466
061622	Sevier St. – Geyer Springs Rd. (Conc. Pvmnt. Pres.) (S) Addt'l Rte.-Sec.: Pulaski 30-23	30	22	Resurface & Shoulder	Under Construction	Feb. 2022	Late 2023	10.34	\$25,075,834	16.72	\$40,548,158
061629*	Newcomb Dr. Sidewalks (Benton) (S)	New		Enhancement	Completed	Sep. 2020	Jun. 2021	-	\$216,979	-	\$216,979
061632	Hwy. 183 – Pulaski Co. Line (Widening) (Bryant) (S)	5	8	Major Widening	Scheduled	2024		3.21	\$15 - \$20 M	3.21	\$15 - \$20 M
061643*	District 6 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	229	5	Sealing	Programmed			2.10	< \$1 M	69.72	\$1 - \$3 M
061644	I-30 Overpass Str. & Apprs. (Saline Co.) (S)	30	22	Structure & Approaches	Scheduled	Jan. 2025		-	\$3 - \$5 M	-	\$3 - \$5 M
061646	South St. – I-430 (Frontage Rd.) (S) Addt'l Rte.-Sec.: Pulaski 30-23	30	22	Resurfacing	Scheduled	Feb. 2023		21.91	\$5 - \$10 M	26.76	\$5 - \$10 M
061671*	Saline Co. Old River Bridge (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061674*	Benton Saline River Trails (RTP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061675	Hwys. 35 & 88 Impvts. (Benton) (S) Addt'l Rte.-Sec.: Saline 88-7	35	1	Resurfacing	Scheduled	Apr. 2023		4.92	\$1 - \$3 M	4.92	\$1 - \$3 M
061678	Hwy. 35 – Hwy. 5 (S)	183	1	Resurfacing	Scheduled	2024		8.83	\$3 - \$5 M	8.83	\$3 - \$5 M
061680	Grant Co. Line – Hwy. 67 (S)	229	4	Resurfacing	Scheduled	2024		9.25	\$3 - \$5 M	9.25	\$3 - \$5 M
061681	I-30 – King Rd. (S)	229	5	Resurfacing	Scheduled	2023		2.13	< \$1 M	2.13	< \$1 M
061698*	Downtown to BHS Connection (Benton) (S)			Enhancement	Under Construction	Sep. 2021		-	\$368,017	-	\$368,017
061699*	Bryant Pkwy. Trail (S)			Enhancement	Completed	May. 2021	Dec. 2021	-	\$290,000	-	\$290,000
061701*	County Line Rd. Walking Trail (Shannon Hills) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061705*	Bryant Pkwy. Extension (S)	CS		Enhancement	Under Construction	May. 2022		-	\$20,777,919	-	\$20,777,919

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

SALINE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
061708*	I-30 Ramp & Frontage Rd. Impvts. (Benton) (S) Addt'l Rte.-Sec.: Saline 5-7	30	22	Frontage Road	Scheduled	2023		-	\$5 - \$10 M	-	\$5 - \$10 M
061709*	Overhead Sign Strs. & Signs Replacement (Central AR) (S) Addt'l Rte.-Sec.: Garland 70-9, 270-5/6; Pulaski 30-23, 440-2	30	22	Safety Improvements	Under Construction	May. 2021	Mid 2023	-	\$210,039	-	\$1,680,308
061717*	Congo Rd./Shenandoah Rd. Roundabout (Benton) (S)	CS		Safety Improvements	Programmed			-	< \$1 M	-	< \$1 M
061718*	Southwest Trail (Saline Co.) (S)			Enhancement	Programmed			-	\$3 - \$5 M	-	\$3 - \$5 M
061727*	Benton Smithers Dr. Sidewalk (TAP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061728*	Saline Crossing Trailhead (TAP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061750	Rockport – Hwy. 70 (S) Addt'l Rte.-Sec.: Hot Spring 30-21	30	22	Resurfacing	Scheduled	Jan. 2024		5.29	\$1 - \$3 M	10.75	\$3 - \$5 M
061754*	Overhead Sign Strs. & Signs Replacement (Central AR) (2022) (S) Addt'l Rte.-Sec.: Hot Spring 30-21; Pulaski 30-23, 440-1	30	22	Safety Improvements	Scheduled	Sep. 2022		-	\$1 - \$3 M	-	\$1 - \$3 M
061756*	Shannon Hills Drive Bridge Replacement (S)	CS		Structure & Approaches	Programmed			-	< \$1 M	-	< \$1 M
061758*	Southwest Trail: Hazel St. – Saline River (Benton) (S)			Enhancement	Programmed			-	\$1 - \$3 M	-	\$1 - \$3 M
061761	Bingham Rd. – Grant Co. Line (S) Addt'l Rte.-Sec.: Pulaski 530-1/3	530	2	Resurfacing	Programmed			3.30	\$1 - \$3 M	7.32	\$5 - \$10 M
A60007*	District 6 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	229	4	Resurfacing	Completed		Jun. 2022	6.00	\$132,186	49.36	\$1,159,267
A60011	Hwy. 183 – Grant Co. Line (Sel. Secs.) (S)	35	1	Resurfacing	Under Construction	May. 2022	Late 2022	5.37	\$2,750,280	5.37	\$2,750,280
A60013	Hwy. 70 – Hwy. 5 (S) Addt'l Rte.-Sec.: Garland 128-11	128	11	Resurfacing	Under Construction	Feb. 2022	Late 2022	0.30	\$152,145	8.38	\$4,249,903
A60020*	District 6 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	30	22	Resurfacing	Programmed			24.27	< \$1 M	69.05	\$1 - \$3 M
BB0602	Hwy. 70 – West (Westbound Lanes) (F)	30	22	Reconstruction	Completed	Mar. 2015	Mar. 2016	2.90	\$11,836,454	2.90	\$11,836,454
BB0614	Bingham Rd. – Grant Co. Line (S) Addt'l Rte.-Sec.: Pulaski 530-1/3	530	2	Resurfacing	Completed	Nov. 2012	Aug. 2014	3.29	\$6,299,796	7.49	\$14,342,087
BR6207*	North Fork Saline River Strs. & Apprs. (S)	CR		Structure & Approaches	Completed	Jul. 2013	Nov. 2015	0.87	\$1,983,586	0.87	\$1,983,586
C62001*	Bryant Shpringill Rd Overly (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jun. 2015	Sep. 2015	3.08	\$468,645	3.08	\$468,645
C62002*	Shannon Hills Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Sep. 2014	Dec. 2014	4.16	\$484,780	4.16	\$484,780
C62003*	Benton & Bauxite Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jun. 2015	Sep. 2015	3.96	\$574,276	3.96	\$574,276
C62004*	Haskell Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jun. 2016	Oct. 2016	3.39	\$315,494	3.39	\$315,494

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

SALINE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
C62005*	Traskwood Overlay (Sel. Secs.)(s)	CS		Resurfacing	Completed	Apr. 2017	Aug. 2017	2.38	\$242,956	2.38	\$242,956
C62007*	Shannon Hills Overlay No. 2 (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jul. 2018	Nov. 2018	2.27	\$377,045	2.27	\$377,045
C62008*	Benton Overlay (S)	CS		Resurfacing	Completed	Jan. 2020	Apr. 2020	2.16	\$399,892	2.16	\$399,892
C62009*	Haskell Overlay & Surfacing (S)	CS		Resurfacing	Under Construction	Jan. 2022	<i>Late 2022</i>	1.56	\$353,003	1.56	\$353,003
C62010*	Bauxite Overlay (S)	CS		Resurfacing	Completed	Feb. 2021	Sep. 2021	2.00	\$256,933	2.00	\$256,933
C62011*	Bryant Overlay (S)	CS		Resurfacing	Completed	Jun. 2021	Nov. 2021	2.22	\$452,332	2.22	\$452,332
C76023*	Alexander Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Oct. 2015	Dec. 2015	1.42	\$432,351	1.42	\$432,351
C76057*	Alexander Overlay No. 2 (S) Addt'l Rte.-Sec.: Pulaski CS	CS		Resurfacing	Completed	Jan. 2020	May. 2020	1.58	\$153,209	1.79	\$306,417
CA0601	Hwy. 70 – Sevier St. (Widening) (F)	30	22	Major Widening Structure & Approaches	Under Construction	Dec. 2018	<i>Mid 2023</i>	5.88	\$187,339,930	5.88	\$187,339,930
CA0610	Hot Springs – I-30 (Widening) (S) Addt'l Rte.-Sec.: Garland 70-9	70	10	Major Widening	Completed	Dec. 2016	May. 2018	6.56	\$29,314,876	17.58	\$78,528,337
EF6202*	Narrows Rd. Flood Damage (2008) (S)	CR		Miscellaneous	Completed		Oct. 2012	-	\$48,476	-	\$48,476
SA6250*	Narrows Rd. Overlay (Sel. Sec.) (S)	CR		Resurfacing	Completed	Jun. 2013	Nov. 2013	3.83	\$419,326	3.83	\$419,326
SA6251*	Co. Rd. 31 - Co. Rd. 33 (Overlay) (S)	CR		Resurfacing	Completed	Feb. 2014	May. 2014	1.26	\$178,976	1.26	\$178,976
SA6252*	Co. Rd. 46 - Co. Rd. 39 (Overlay) (S)	CR		Resurfacing	Completed	Jul. 2015	Nov. 2015	1.90	\$239,397	1.90	\$239,397
SA6253*	Hwy. 367 - Southwest (Overlay) (S)	CR		Resurfacing	Completed	Jun. 2016	Sep. 2016	2.86	\$398,963	2.86	\$398,963
SA6254*	Saline Co. Overlay No. 4 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2017	Oct. 2017	2.79	\$492,623	2.79	\$492,623
SA6255*	Co. Rd. 29 - South (Overlay) (S)	CR		Structure & Approaches	Completed	Sep. 2018	Dec. 2018	4.60	\$500,716	4.60	\$500,716
SA6256*	Saline Co. Overlay No. 5 (S)	CR		Resurfacing	Completed	Feb. 2020	Jun. 2020	13.77	\$1,372,840	13.77	\$1,372,840
SA6257*	Saline Co. Seal (S)	CR		Resurfacing	Completed	Feb. 2020	Aug. 2020	8.43	\$264,990	8.43	\$264,990
Totals For All Projects In Saline County								242.18	\$466,260,247		

* Job not shown on county map.
