


- Status of Improvements
- Programmed
 - Scheduled
 - Under Construction
 - Completed
 - Bridge
 - ◆ Interchange
 - ⊕ Intersection Improvement
 - Slide Repair
 - Roadway
 - New Location

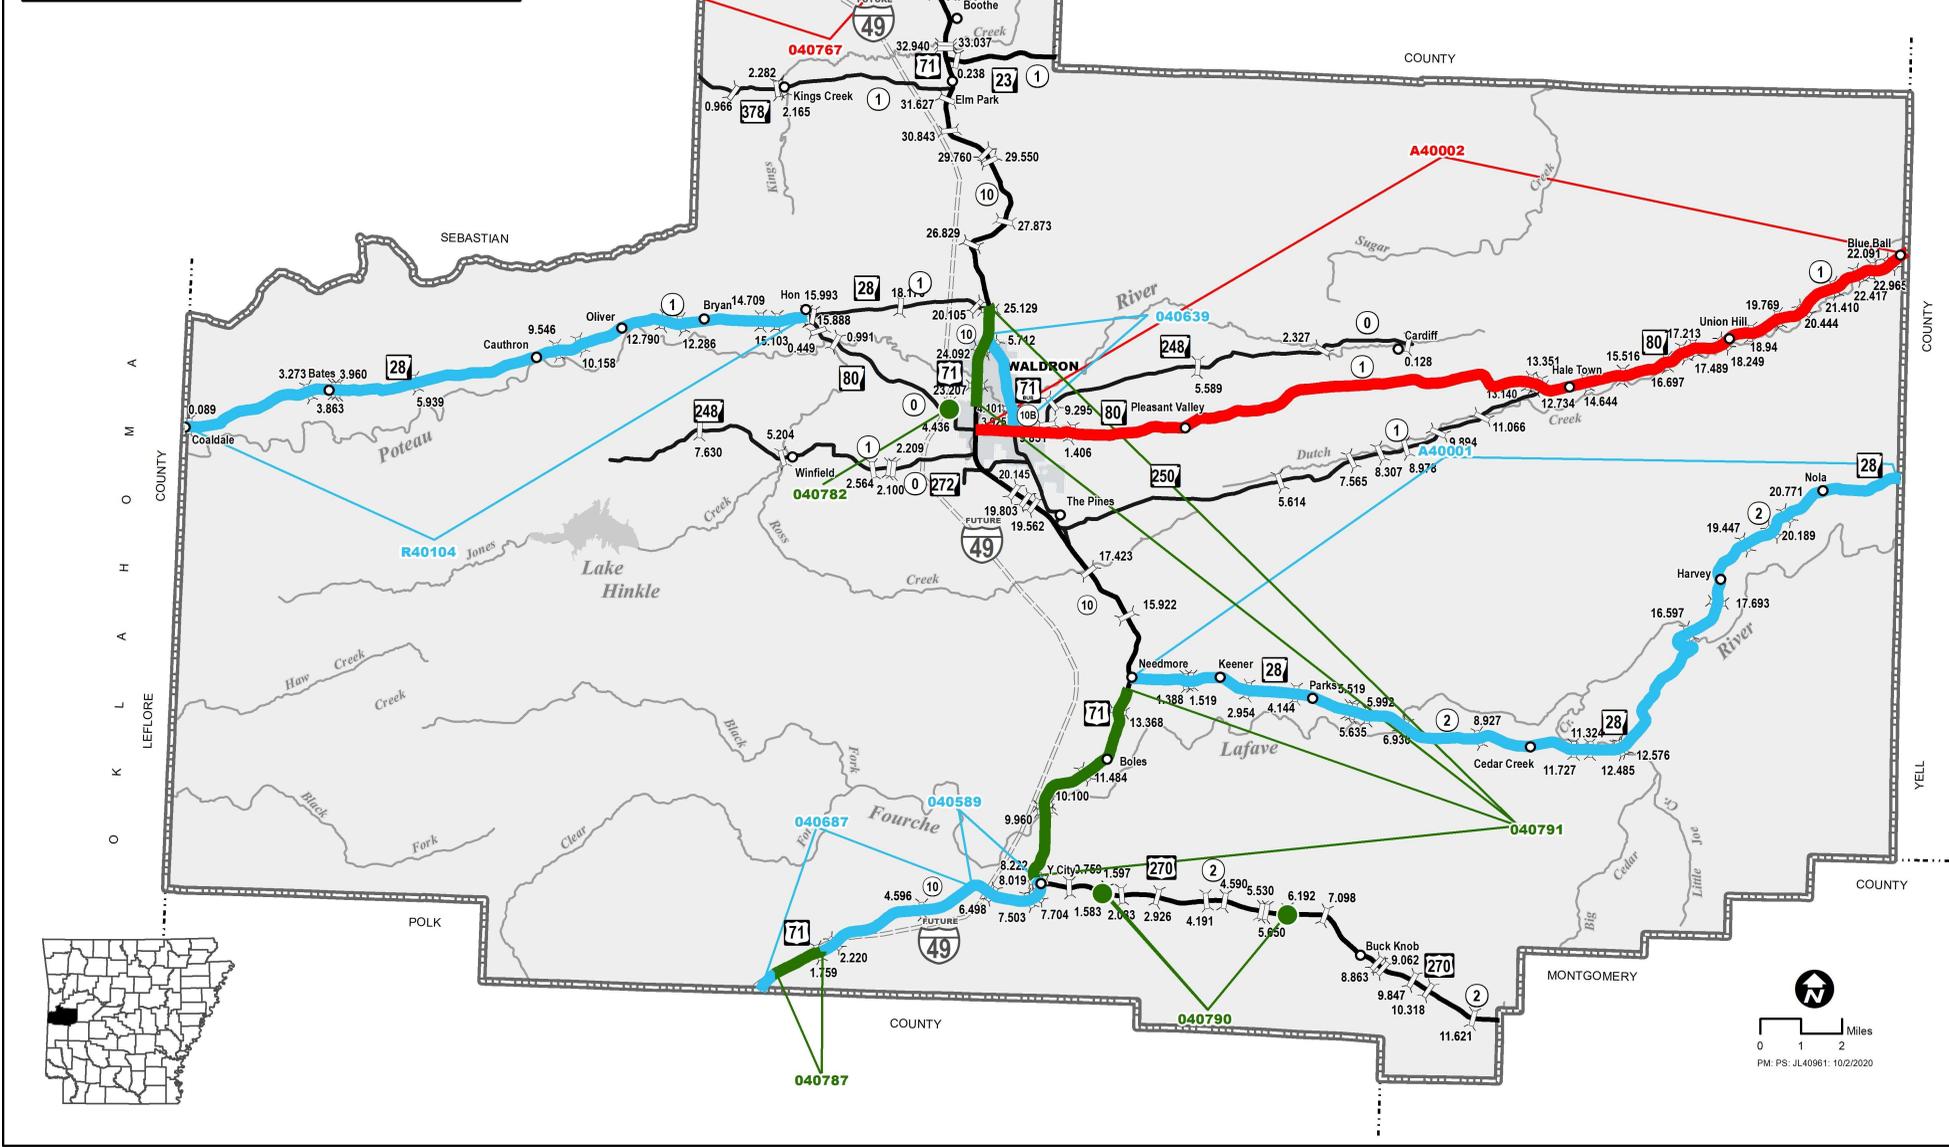

SUMMARY OF CONSTRUCTION PROJECTS

SCOTT COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
012351*	Districts 4, 5, 8 & 9 Bridge Preservation (2020) (S) Addt'l Rte.-Sec.: Various	71	10	Bridge Rehabilitation	Under Construction	May. 2020	Mid 2021	-	\$186,302	-	\$6,147,965
040375*	Hwy. 28 R.R. Surfacing Upgrade (Hon) (S)	28	1	RR Crossing	Completed	Sep. 2001	Aug. 2011	-	\$30,703	-	\$30,703
040589	Mill Creek – South (Overlay) (S)	71	10	Resurfacing	Completed	Apr. 2011	May. 2011	2.27	\$712,825	2.27	\$712,825
040601*	Waldron Sidewalks (ATEP-11) (S)			Enhancement	Completed	Jun. 2013	Dec. 2014	-	\$50,234	-	\$50,234
040639	Hwy. 80 – North (Waldron) (Overlay) (S)	71	10B	Resurfacing	Completed	May. 2012	Sep. 2012	2.63	\$605,205	2.63	\$605,205
040687	Polk Co. Line – North (Hwy. 71) (Overlay) (S)	71	10	Resurfacing	Completed	Feb. 2016	Aug. 2016	5.97	\$1,419,559	5.97	\$1,419,559
040761*	District 4 Sealing Program (2018) (S) Addt'l Rte.-Sec.: Various	270	2	Sealing	Under Construction			4.20	\$100,541	56.33	\$1,348,430
040767	Logan Co. Line – Sebastian Co. Line (S)	71	12	Resurfacing	Under Construction	May. 2020	Oct. 2020	6.56	\$2,346,821	6.56	\$2,346,821
040782	Hwy. 80 Str. & Apprs. (S)	80	0	Structure & Approaches	Scheduled	Jan. 2022		-	< \$1 M	-	< \$1 M
040787	Mena – "Y" City (Passing Lanes) (S) Addt'l Rte.-Sec.: Polk 71-9	71	10	Passing Lanes	Scheduled	Mar. 2022		1.25	\$1 - \$5 M	2.49	\$1 - \$5 M
040790	Spring Branch, Alexander Creek & Relief Strs. & Apprs. (S)	270	2	Structure & Approaches	Scheduled	Jun. 2022		-	\$1 - \$5 M	-	\$1 - \$5 M
040791	Hwy. 270 – Hwy. 28 North (Sel. Secs.) (S)	71	10	Resurfacing	Scheduled	Feb. 2021		8.23	\$1 - \$5 M	8.23	\$1 - \$5 M
040795*	Hwy. 71 RR Signal Upgrade (Waldron) (S)	71	10	RR Crossing	Under Construction			-	\$70,000	-	\$70,000
A40001	Hwy. 71 – Yell Co. Line (S)	28	2	Resurfacing	Sub. Completed	Sep. 2019	Sep. 2020	23.86	\$8,373,336	23.86	\$8,373,336
A40002	Waldron – Yell Co. Line (S) Addt'l Rte.-Sec.: Scott 80-1	80	0	Resurfacing	Under Construction	Sep. 2019	Oct. 2020	24.46	\$8,498,764	24.46	\$8,498,764
C63001*	Waldron 2nd St. Overlay (S)			Resurfacing	Completed	Feb. 2016	May. 2016	0.90	\$164,927	0.90	\$164,927
C76055*	Booneville & Mansfield Overlay (Sel.secs.)(s) Addt'l Rte.-Sec.: Logan CS; Sebastian CS	CS		Resurfacing	Sub. Completed	Jul. 2019	Apr. 2020	-	\$0	-	\$499,824
R40104	Oklahoma State Line – Hon (S) Addt'l Rte.-Sec.: Scott CS	28	1	Minor Widening	Completed	Jul. 2018	Dec. 2019	15.75	\$6,494,596	15.75	\$6,494,596
SA6335*	Scott County Reconstruction No. 2 (S)	CR		Reconstruction	Completed	Jul. 2010	Nov. 2010	2.80	\$907,556	2.80	\$907,556
SA6337*	Scott County Surfacing No 2 (Sel Secs) (S)	CR		Resurfacing	Completed	Jul. 2011	Oct. 2011	2.00	\$170,216	2.00	\$170,216
SA6338*	Scott County Surfacing No. 3 (Sel. Secs.) (S)	CR		Surfacing	Completed	Jul. 2012	Oct. 2012	2.27	\$243,661	2.27	\$243,661
SA6339*	Scott Co Surfacing & Pvmnt Mkgs(sel Secs) (S)	CR		Base	Completed	Sep. 2013	Dec. 2013	1.05	\$133,208	1.05	\$133,208
SA6340*	Scott County Surf. & Drainage(sel. Secs.)(s)	CR		Resurfacing	Completed	Jun. 2014	Oct. 2014	5.34	\$728,527	5.34	\$728,527
SA6341*	Scott County Surfacing No. 4 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Mar. 2016	Aug. 2016	1.66	\$278,188	1.66	\$278,188
SA6342*	Hwy. 28 - Co. Rd. 18 (Reconstruction) (S)	CR		Reconstruction	Completed	Apr. 2017	Aug. 2017	1.12	\$352,063	1.12	\$352,063

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

SCOTT COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or Sub. Comp.</i> Date	<u>County Totals</u>		<u>Project Totals</u>	
								Length (Mi)	Cost	Length (Mi)	Cost
SA6343*	Waldron City Limits-Hwy. 248(LEVL & Resel)(s)	CR		Resurfacing	Completed	May. 2017	Sep. 2017	7.15	\$325,750	7.15	\$325,750
SA6344*	Hwy. 248 - South (Repair & Reseal) (S)	CR		Resurfacing	Completed	May. 2018	Sep. 2019	4.55	\$847,987	4.55	\$847,987
Totals For All Projects In Scott County								124.02	\$39,996,969		

* Job not shown on county map.
